



Drainage Services Department

Port Shelter Sewerage, Stage 3 – Sewerage Works at Po Toi O

Quarterly EM&A Report (Period from Dec 2025 to Feb 2026)

Prepared by

SGS Hong Kong Limited

Certified by:

A handwritten signature in black ink, consisting of a large, stylized 'H' and 'J'.

Johnathan Ho

Verified by:

A handwritten signature in black ink, consisting of a cursive 'F.C. Tsang'.

F.C. Tsang

Environmental Team Leader Independent Environmental Checker

Our Ref: PL - 202607047

Drainage Services Department
Special Duty Division
42/F, Revenue Tower, 5 Gloucester Road,
Wan Chai, Hong Kong.

Attention: Mr. Marcus LEUNG

29 July 2026

Dear Mr. Leung,

Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O
Quarterly EM&A Report for December 2025 to February 2026

Reference is made to your submission of the Quarterly EM&A Report for December 2025 to February 2026 (Revision 01). We are pleased to inform you that we have no adverse comment on the captioned report.

Thank you for your attention. Please do not hesitate to contact the undersigned should you have any queries.

Yours faithfully,



F.C. Tsang
Independent Environmental Checker

cc. ETL – Johnathan HO



Drainage Services Department
Port Shelter Sewerage, Stage 3 – Sewerage
Works at Po Toi O
Quarterly EM&A Report
(Period from December 2025 to February 2026)

Prepared by

SGS Hong Kong Limited

Drainage Services Department

SGS Hong Kong Ltd. Units 303 & 305, 3/F, Building 22E
Phase 3, Hong Kong Science Park
Pak Shek Kok, New Territories
Hong Kong, China

Issue and Revision Record

Revision	Description	Prepared by	Checked by	Approved by	Date
01	Submission	Various	Johnathan Ho 	Roy Hung 	Mar 2026

Disclaimer

This document is issued by the Company under its General Conditions of Service accessible at <http://www.sgs.com/en/Terms-and-Conditions.aspx>. Attention is drawn to the limitation of liability, indemnification and jurisdiction issues defined therein.

Any holder of this document is advised that information contained hereon reflects the Company's findings at the time of its intervention only and within the limits of Client's instructions, if any. The Company's sole responsibility is to its Client and this document does not exonerate parties to a transaction from exercising all their rights and obligations under the transaction documents. Any unauthorized alteration, forgery or falsification of the content or appearance of this document is unlawful and offenders may be prosecuted to the fullest extent of the law.

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	3
		Ref#	EMA2403/03/65
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

TABLE OF CONTENT

1. EXECUTIVE SUMMARY	4
2. INTRODUCTION	5
3. SUMMARY OF EM&A MONITORING REQUIREMENTS	5
4. SUMMARY OF EM&A MONITORING RESULTS	8
5. WASTE MANAGEMENT.....	11
6. ENVIRONMENTAL NON-CONFORMANCE	12
7. COMMENTS, RECOMMENDATIONS AND CONCLUSION	13
APPENDIX A - LOCATION OF THE MONITORING AND CONTROL STATIONS.....	A1
APPENDIX B - LAYOUT PLAN OF PROJECT AREA	B1
APPENDIX C - PROJECT ORGANIZATION CHART & CONTACT INFORMATION OF KEY PERSONNEL	C1
APPENDIX D – CONSTRUCTION WORK PROGRAMME	D1
APPENDIX E - IMPLEMENTATION OF RECOMMENDED MITIGATION MEASURES.....	E1
APPENDIX F - METEOROLOGICAL DATA EXTRACTED FROM HONG KONG OBSERVATORY	F1
APPENDIX G - GRAPHICAL PLOTS OF THE MONITORING RESULT	G1
APPENDIX H - SUMMARY OF WASTE FLOW TABLE	H1
APPENDIX I - CUMULATIVE STATISTICS ON COMPLAINTS, NOTIFICATIONS OF SUMMONS.....	I1

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	4
		Ref#	EMA2403/03/65
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

1. EXECUTIVE SUMMARY

- 1.1 This Quarterly Environmental Monitoring & Audit (EM&A) report presents the EM&A works performed in the period between December 2025 to February 2026 for “Port Shelter Sewerage, Stage 3 – Sewerage works at Po Toi O”.
- 1.2 The impact stage EM&A Programme for the Project includes air quality, noise, water quality, waste, ecology, fisheries, landscape and visual and built heritage monitoring. The recommended environmental mitigation measures were implemented on site and regular inspections were carried out to ensure that the environmental conditions are acceptable.
- 1.3 The EM&A programme was carried out by the ET in accordance with the EM&A Manual requirements. It is concluded from the EM&A works that adequate environmental mitigation measures have been implemented by the contractor where appropriate in the reporting quarter.
- 1.4 The construction commencement date of the project was revised on 27 April 2021. The construction commencement date of provision of village sewerage to the unsewered areas of Po Toi O has been revised from 1 March 2021 to 16 June 2021, and the construction commencement date of village sewerage construction of the local sewage treatment plant (STP) has been revised from 10 May 2021 to 16 June 2021. In view of the revised construction commencement date, the EM&A programme was subsequently suspended from 28 April 2021 until 16 June 2021.

Exceedance of Action and Limit Level

- 1.5 There was no action or limit level exceedance record of construction noise and air quality was recorded in the reporting quarter.

Implementation of Mitigation Measures

- 1.6 Construction phase weekly site inspections were carried out to confirm the implementation measures undertaken by the Contractor in the reporting quarter. The status of implementation of mitigation measures during the reporting quarter is shown in **Appendix E**.

Record of Complaints

- 1.7 No complaints, notification of summons and successful prosecution was received in the reporting period. No public engagement activity was conducted in the reporting quarter.
- 1.8 No air quality, noise and water complaints during 0700 – 1900 hours on normal weekdays was received in the reporting quarter.

Record of Notification of Summons and Successful Prosecutions

- 1.9 No notification of summons and successful prosecution was received in the reporting period. No public engagement activity was conducted in the reporting quarter.

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	5
		Ref#	EMA2403/03/65
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

2. INTRODUCTION

Project Information

- 2.1 Société Générale de Surveillance (SGS) Hong Kong Limited has been appointed by Drainage Services Department (DSD) as the Environmental Team (ET) to undertake the EM&A programme during construction phase of the Project in accordance to the approved EM&A Manual for the proposed sewerage works in Po Toi O (hereafter as “The Project”), an environmental enhancement project that aims to improve environmental hygiene of the Po Toi O area.
- 2.2 The Quarterly EM&A Report is prepared in accordance with the Section 13.6 of the EM&A Manual. This Quarterly EM&A Report presents the monitoring work conducted from 1 December 2025 to 28 February 2026. The purpose of this report is to summary the findings in the EM&A of the project over the reporting quarter.

Project Organization

- 2.3 The project organization chart, key personnel contact names and numbers and lines of communication with respect to the onsite environmental management performce is shown in **Appendix C**.

Environmental Status in the Reporting Quarter

- 2.4 During the reporting quarter, construction works at Po Toi O undertaken include:

- Major activities in the reporting quarter:

1. Construction of village sewer;
2. E&M works for Po Toi O Sewage Treatment Plant

- Major activities in the upcoming quarter:

1. Construction of village sewer;
2. TBM;
3. E&M works for Po Toi O Sewage Treatment Plant

- 2.5 The Construction Works Programme of the Project is provided in **Appendix D**.

3. SUMMARY OF EM&A MONITORING REQUIREMENTS

- 3.1 In accordance with the EM&A Manual, environmental parameters including air quality, noise & water quality have been monitored in the reporting quarter. The specific parameters, monitoring

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	6
		Ref#	EMA2403/03/65
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

frequency and the respective Action and Limit levels are given in **Table 3-1** and **Table 3-2**. Locations of the monitoring stations are provided in **Appendix A**.

Table 3-1 Summary of Impact EM&A Requirements (Air & Noise)

Parameters ²	Descriptions	Locations ¹	Frequencies	Action Level	Limit Level
Air Quality	24-hour TSP	AMS1N	At least once every 6 days	153 µg/m ³	260 µg/m ³
	24-hour TSP	AMS2N1		179 µg/m ³	
	24-hour TSP	AMS3N		158 µg/m ³	
	24-hour TSP	AMS4N		144 µg/m ³	
	1-hour TSP	AMS1N		319 µg/m ³	500 µg/m ³
	1-hour TSP	AMS2N1		279 µg/m ³	
	1-hour TSP	AMS3N		303 µg/m ³	
	1-hour TSP	AMS4N		278 µg/m ³	
Noise	Leq, 30 minutes	NMS1N	At least once per week	When one documented complaint is received from any one of the noise sensitive receivers	75 dB(A)*
	Leq, 30 minutes	NMS2N1			
	Leq, 30 minutes	NMS3N			
	Leq, 30 minutes	NMS4N			

Notes:

1- Due to several limitations (i.e. EM&A approved monitoring stations not accessible) identified at the air quality and noise monitoring stations in the Approved EM&A Manual for the Project, the monitoring location AMS1 – AMS4 & NMS1 – NMS4 were replaced by alternative monitoring location AMS1N – AMS4N & NMS1N – NMS4N, which was approved by ER and IEC.

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	7
		Ref#	EMA2403/03/65
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

Table 3-2 Summary of Impact EM&A Requirements (Water Quality)

Parameters ²	Descriptions	Locations ¹	Frequencies	DO AL	TUBIDITY AL	SS AL	DO LL	TUBIDITY LL	SS LL
Water Quality	Turbidity (NTU) DO (mg/L and % Of Saturation) SS (mg/L)	WMS1N	3 Days Per Week (The Interval Between Two Sets of Monitoring Shall Not Be Less Than 36 Hours.)	7.57 (S&M) 7.50 (B)	1.11	10	7.55 (S&M) 7.45 (B)	1.90	12
		WMS2N		7.58 (S&M) 7.49 (B)	1.60	9	7.51 (S&M) 7.36 (B)	2.50	12
		WMS3		7.62 (S&M)	1.30	10	7.49 (S&M)	1.50	12
		WMS4		7.73 (S&M)	1.47	9	7.53 (S&M)	1.75	10
		WMS5		7.62 (S&M)	1.50	8.65	7.60 (S&M)	1.70	12
		WMS6		7.56 (S&M) 7.41 (B)	1.40	9	7.42 (S&M) 7.37 (B)	1.70	11
		I1		7.52 (S&M) 7.50 (B)	1.55	11.45	7.40 (S&M) 7.44 (B)	2.03	15
		I2		7.59 (S&M) 7.53 (B)	1.15	10	7.04 (S&M) 7.51 (B)	1.80	12

Environmental Mitigation Measures

3.2 Environmental mitigation measures have been recommended in the EM&A Manual. Summary implementation status of the environmental mitigation measures is provided in **Appendix E**.

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	8
		Ref#	EMA2403/03/65
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

4. SUMMARY OF EM&A MONITORING RESULTS

4.1 In accordance with the EM&A Manual, impact monitoring has been conducted in the reporting quarter. Meteorological data for the reporting quarter have been extracted from Hong Kong Observatory and present in **Appendix F**. Monitoring data with graphical presentation for the reporting quarter are show in **Appendix G**. A Summary on the monitoring results is presented in **Table 4-1**.

Table 4-1 Summary of Monitoring Data

Parameter ¹	Monitoring Location	Minimum	Maximum	Average
Air Quality				
24-hour TSP	AMS1N	25 µg/m ³	57 µg/m ³	38.6 µg/m ³
24-hour TSP	AMS2N1	21 µg/m ³	52 µg/m ³	37.5 µg/m ³
24-hour TSP	AMS3N	27 µg/m ³	51 µg/m ³	39.1 µg/m ³
24-hour TSP	AMS4N	19 µg/m ³	51 µg/m ³	28.7 µg/m ³
1-hour TSP	AMS1N	31 µg/m ³	102 µg/m ³	43.6 µg/m ³
1-hour TSP	AMS2N1	30 µg/m ³	74 µg/m ³	40.7 µg/m ³
1-hour TSP	AMS3N	24 µg/m ³	70 µg/m ³	40.0 µg/m ³
1-hour TSP	AMS4N	19 µg/m ³	68 µg/m ³	31.4 µg/m ³
Construction Noise				
Leq(30min)	NMS1N	54.9 dB(A)	65.3 dB(A)	62.6 dB(A)
Leq(30min)	NMS2N1	55.3 dB(A)	60.3 dB(A)	58.4 dB(A)
Leq(30min)	NMS3N	56.1 dB(A)	63.1 dB(A)	59.9 dB(A)
Leq(30min)	NMS4N	49.8 dB(A)	63.3 dB(A)	59.3 dB(A)

Remarks:

1. A correction of +3 dB(A) was made to the free field measurements.

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	9
		Ref#	EMA2403/03/65
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

Other Influencing Factors of the Monitoring Results

Air quality monitoring

4.2 Major emission sources during air quality monitoring in the reporting quarter were mainly vehicle emission from Po Toi O Chuen Road and nearby residents' activities.

Noise monitoring

4.3 Major noise sources during noise monitoring in the reporting quarter were mainly road traffic noise.

Monitoring Exceedances

4.4 Summary of the exceedances in the reporting quarter is tabulated in **Table 4-2** and **Table 4-3**.

Table 4-2 Exceedance Summary for Air and Noise Monitoring

Monitoring Station	Parameter	No. of Exceedance		Action Taken
		Action Level	Limit Level	
Air Quality				
AMS1N	24-hour TSP	0	0	N/A
AMS2N1	24-hour TSP	0	0	N/A
AMS3N	24-hour TSP	0	0	N/A
AMS4N	24-hour TSP	0	0	N/A
AMS1N	1-hour TSP	0	0	N/A
AMS2N1	1-hour TSP	0	0	N/A
AMS3N	1-hour TSP	0	0	N/A
AMS4N	1-hour TSP	0	0	N/A
Construction Noise				
NMS1N	Leq(30min)	0	0	N/A

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	10
		Ref#	EMA2403/03/65
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

NMS2N1	Leq(30min)	0	0	N/A
NMS3N	Leq(30min)	0	0	N/A
NMS4N	Leq(30min)	0	0	N/A

1-hour TSP Monitoring

- 4.5 All 1-hour TSP monitoring was conducted as scheduled in the reporting quarter. No action/ limit level exceedance was recorded.

24-hour TSP Monitoring

- 4.6 All 24-hour TSP monitoring was conducted as scheduled in the reporting quarter. No action/ limit level exceedance was recorded.

Construction Noise Monitoring

- 4.7 All construction noise monitoring was conducted as scheduled in the reporting quarter. No action/ limit level exceedance was recorded.

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	11
		Ref#	EMA2403/03/65
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

5. WASTE MANAGEMENT

- 5.1 As advised by the Contractor, 0 m³ of inert C&D material was generated and disposal to Tseung Kwan O Area 137 Fill Bank (TKO137FB) in the reporting quarter. For C&D wastes, 0 tonnes of general refuse was disposed of at NENT landfill, 0 kg waste were collected by recycling contractors, and 0 kg of chemical wastes was collected by licensed Contractors in the reporting quarter.
- 5.2 The detailed Summary of waste flow is show in **Appendix H**.

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	12
		Ref#	EMA2403/03/65
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

6. ENVIRONMENTAL NON-CONFORMANCE

- 6.1 For this reporting quarter, no environmental complaint was received.
- 6.2 No non-compliance and environmental related prosecution or notification of summons was received. There was no breach of Action or Limit Levels for Air Quality and Noise monitoring in the reporting quarter. Exceedance of suspended solids (SS) were recorded, investigated and no project related exceedances were identified.
- 6.3 Statistics on complaints, notifications of summons, successful prosecutions and public engagement activities are summarized in **Appendix I**.

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	13
		Ref#	EMA2403/03/65
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

7. COMMENTS, RECOMMENDATIONS AND CONCLUSION

Comments

- 7.1 Based on the observations made during site audits and construction dust and noise monitoring results, no non-compliances and exceedances of air quality and noise limits were recorded. Water quality exceedances were recorded and investigated and no project related exceedances were recorded.

Recommendations


- 7.2 Reviewing the implementation of the recommended mitigation measures in the EM&A Manual, it was observed that they were effective and efficient in controlling the potential impacts due to construction of the project during the reporting quarterly. Review of the effectiveness and efficiency of the EM&A programme will continue, and recommendations will be provided to remediate any potential impact due to the project and to improve the EM&A programme if deficiencies of the existing EM&A programme are identified.


Conclusion

- 7.3 The EM&A programme as recommended in the EM&A Manual has been undertaken since the construction works of Port Shelter Sewerage, Stage 3 – Sewerage works at Po Toi O works commenced on 1 March 2021.
- 7.4 Monitoring of air quality and noise with respect to the Project is underway. In particular, the 1-hour TSP, 24-hour TSP, noise level (as Leq, 30 minutes). There was no breach of Action and Limit Levels for 1-hour TSP, 24-hour TSP and noise monitoring in the reporting quarter.
- 7.5 No complaint was received during the reporting quarter.
- 7.6 No notifications of summons or successful prosecution were received during the reporting quarter.

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	A-1
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

APPENDIX A - LOCATION OF THE MONITORING AND CONTROL STATIONS

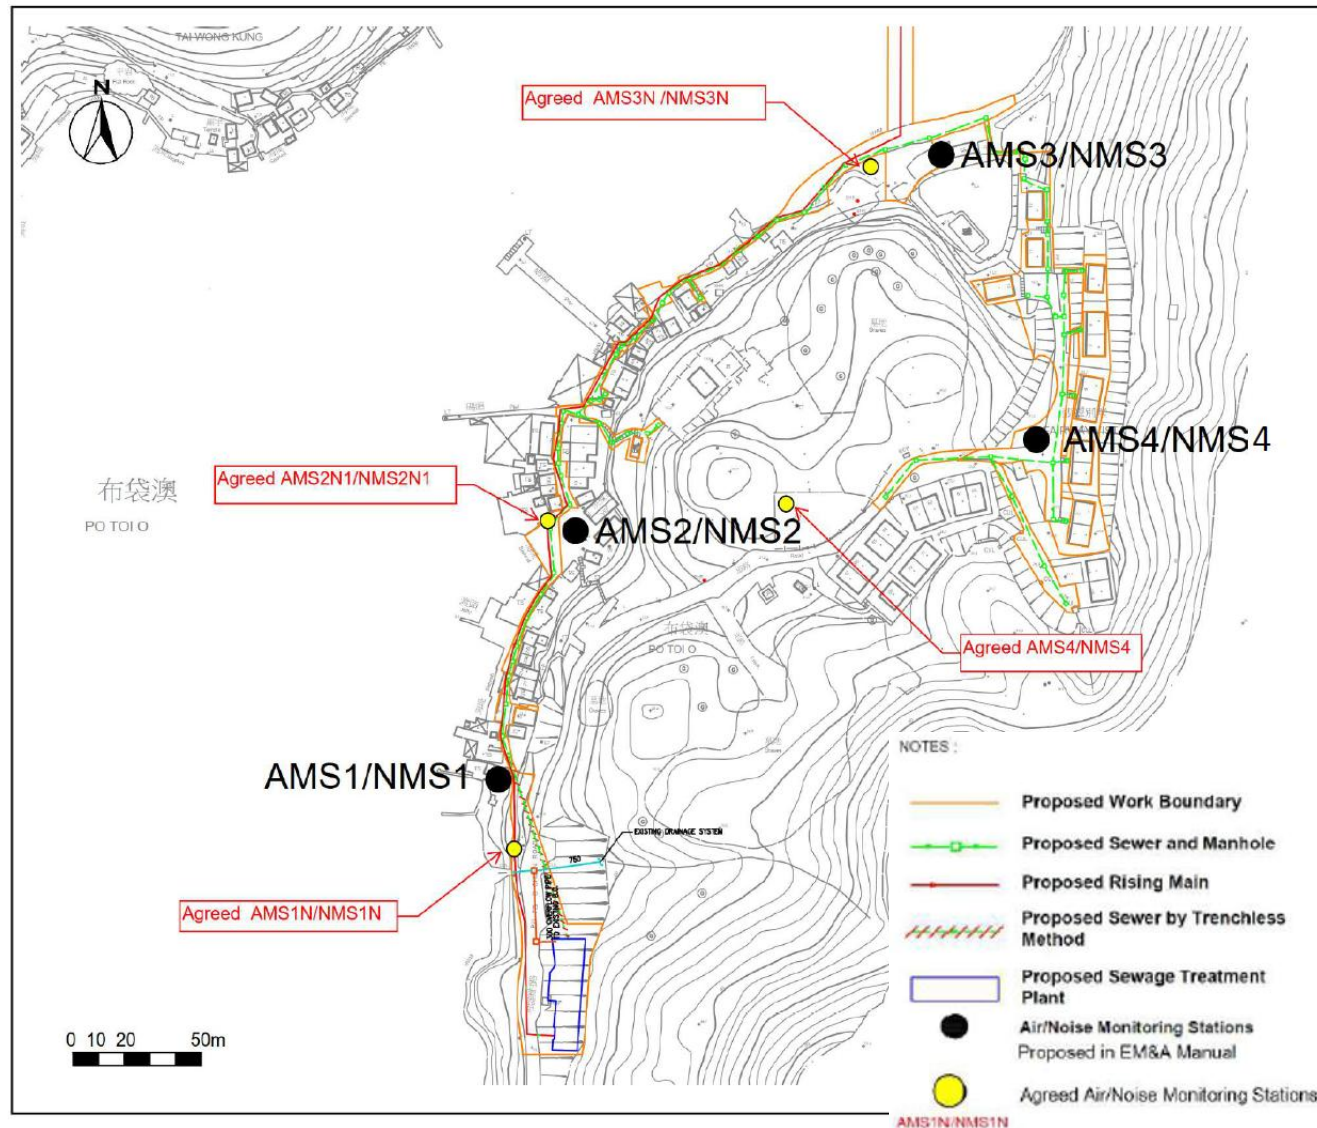


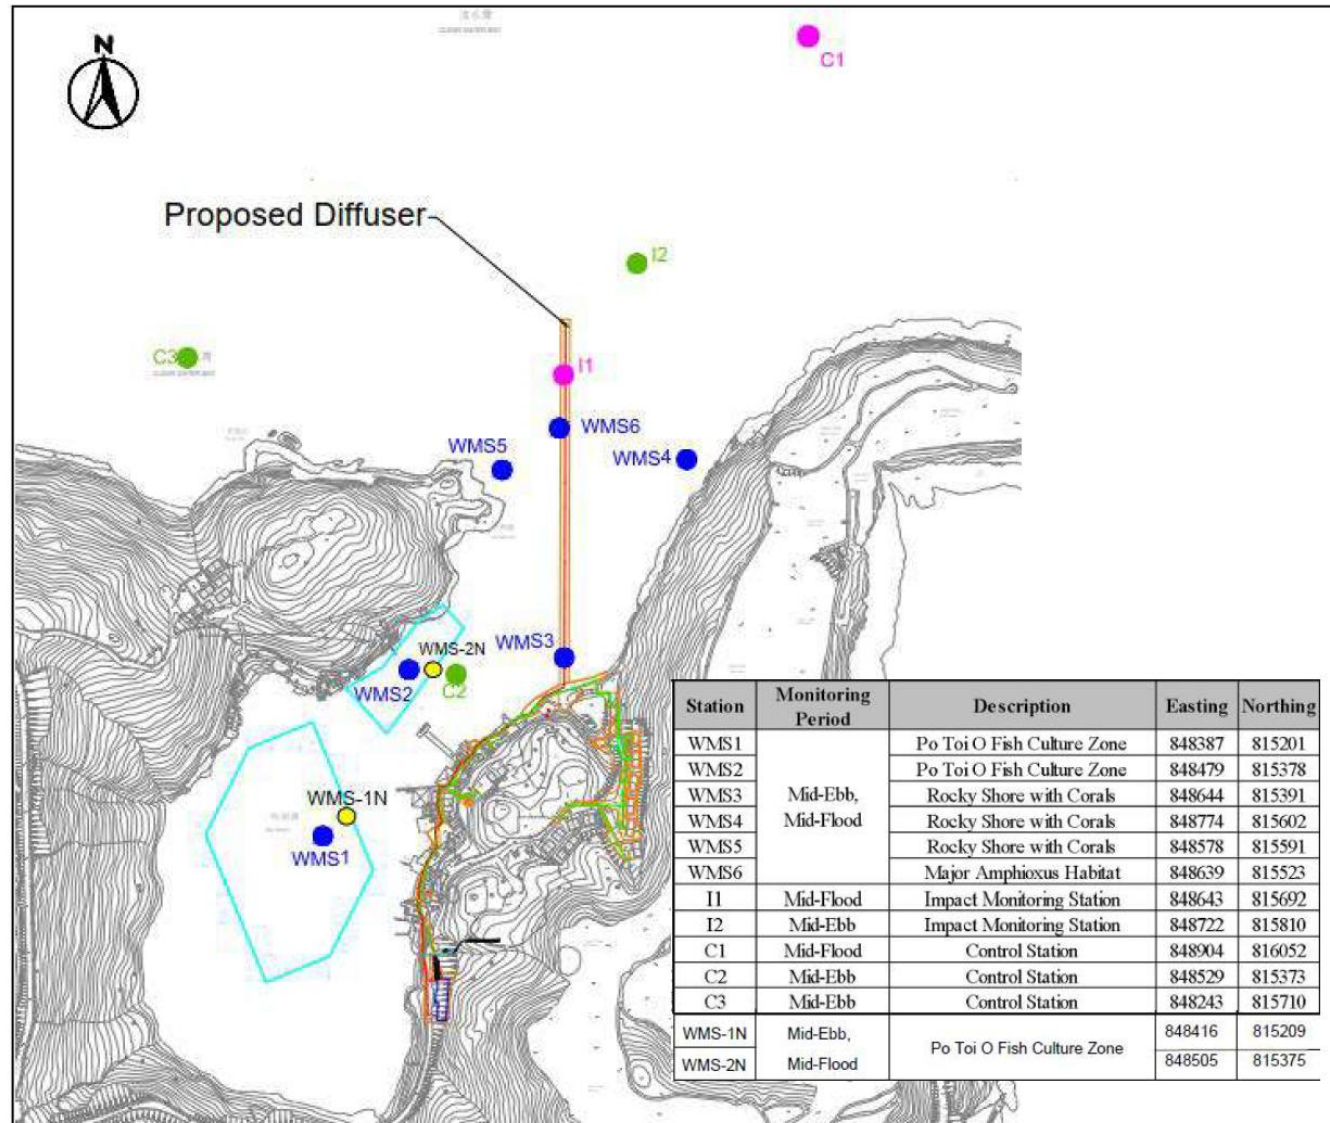

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		Page	B-1
			Ref#	-
	Quarterly EM&A Report		Rev.	01
			Date	Mar 26

APPENDIX B - LAYOUT PLAN OF PROJECT AREA


	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		Page	B-2
			Ref#	-
	Quarterly EM&A Report		Rev.	01
			Date	Mar 26

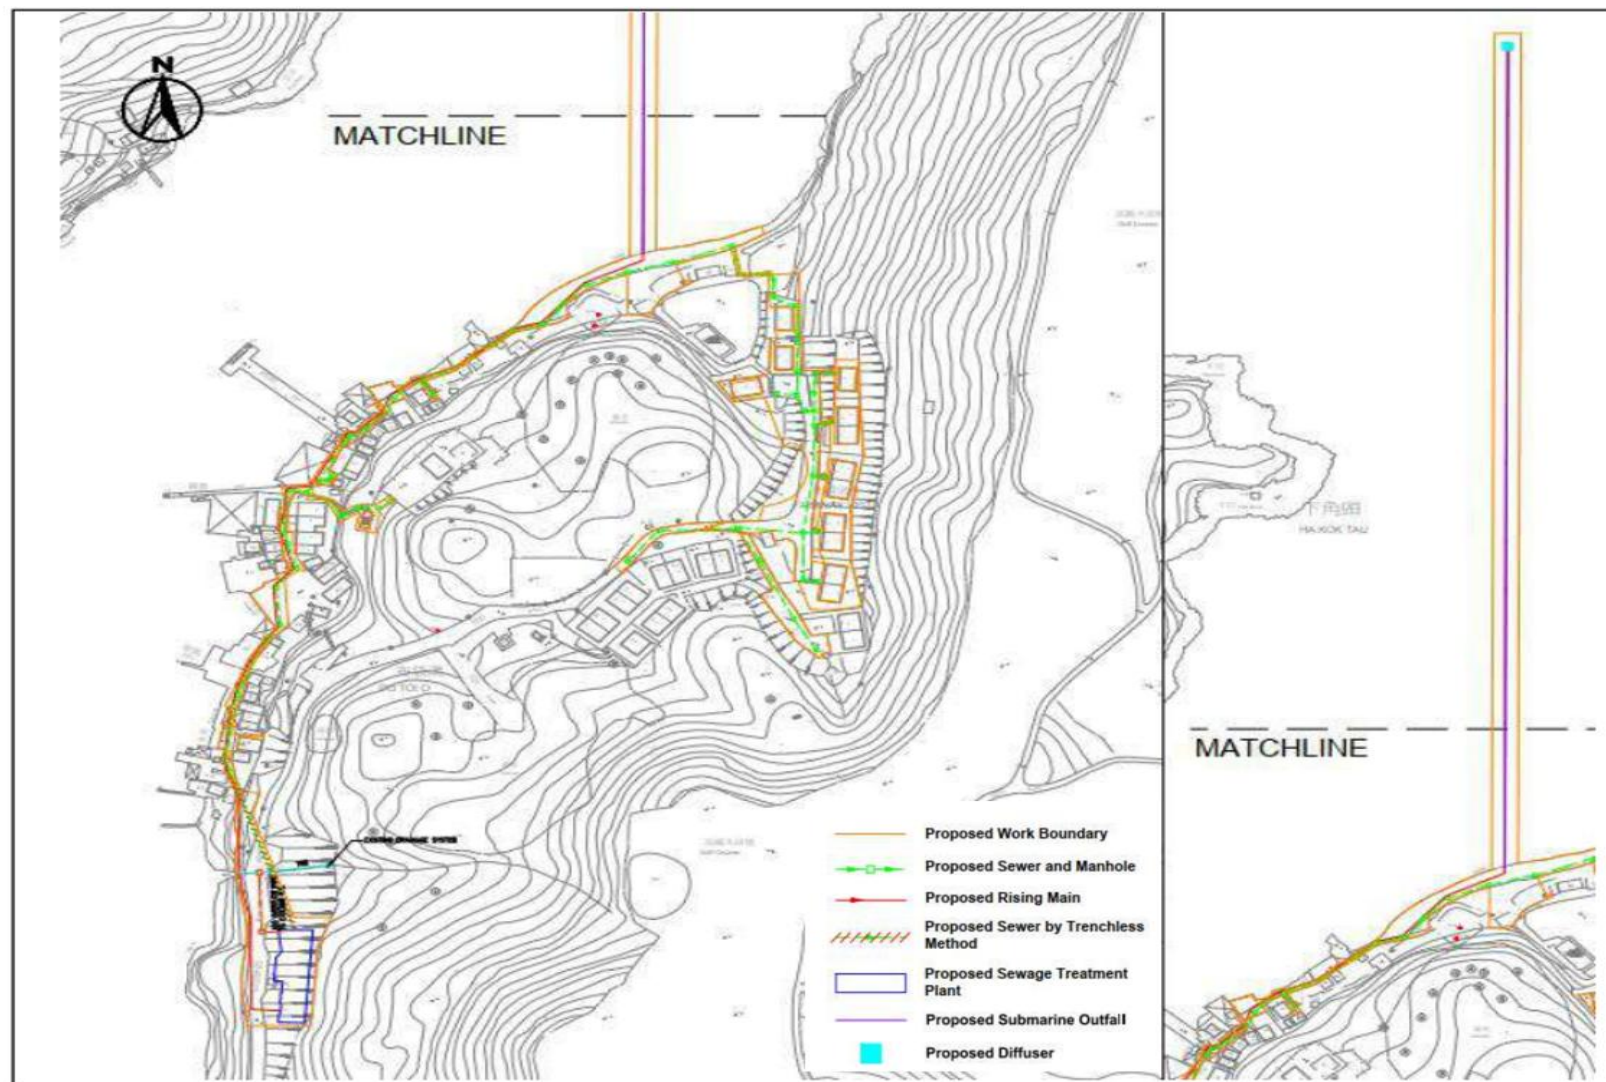

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	C-1
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

APPENDIX C - PROJECT ORGANIZATION CHART & CONTACT INFORMATION OF KEY PERSONNEL

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		Page	C-2
	Quarterly EM&A Report		Ref#	-
			Rev.	01
			Date	Mar 26

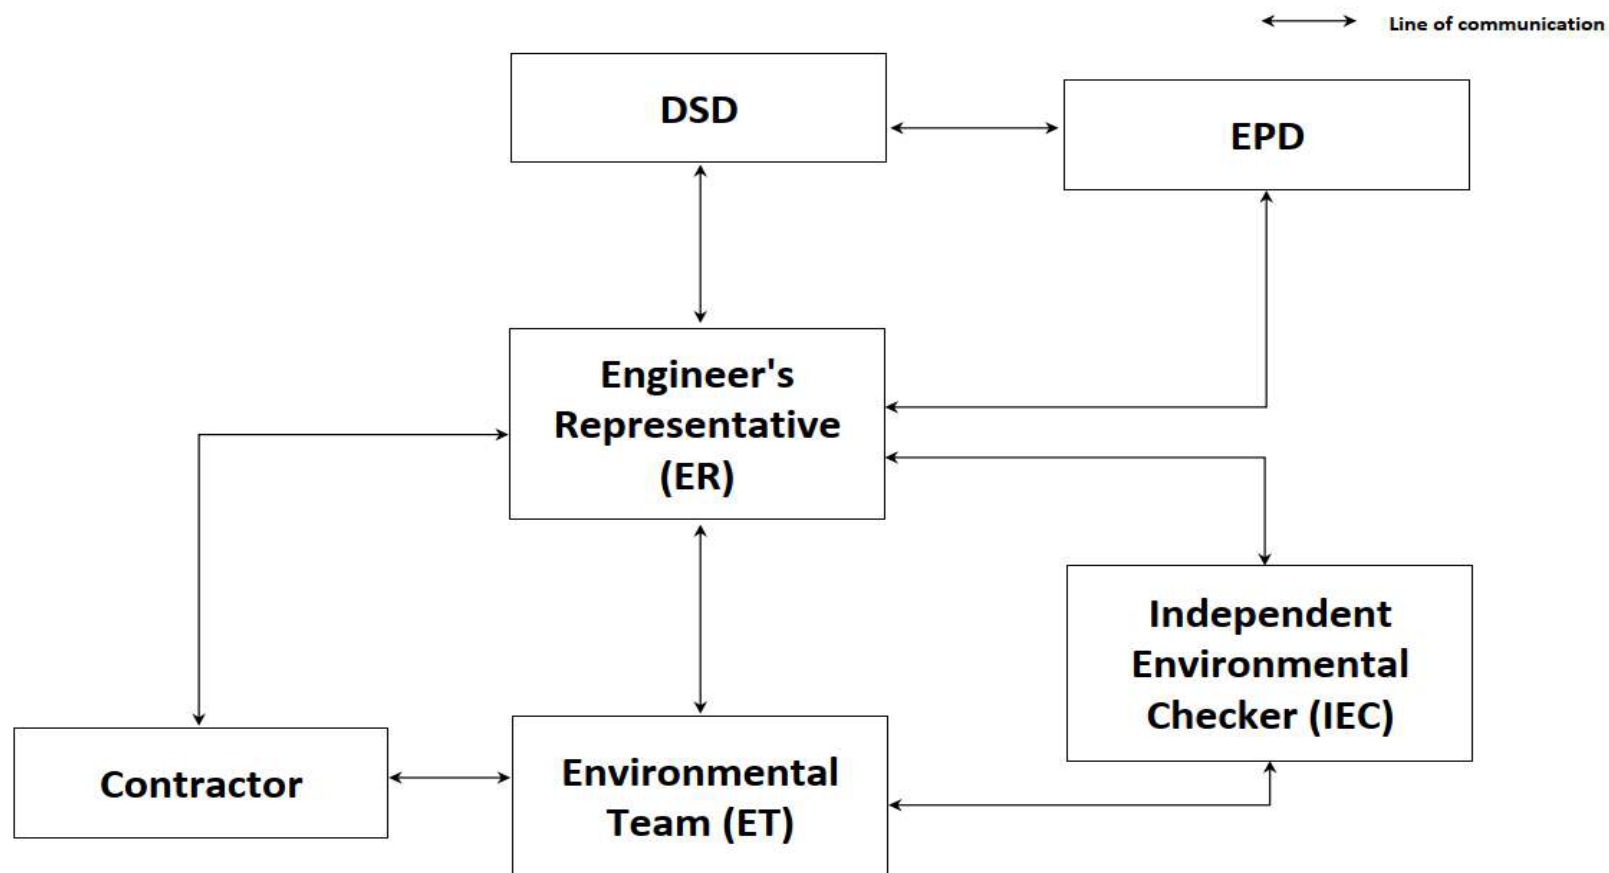


	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		Page	C-2
			Ref#	-
	Quarterly EM&A Report		Rev.	01
			Date	Mar 26

Position	Party	Name	Telephone
Project Proponent	Drainage Services Department (DSD)	Mr. Gary Chung	2594 7227
Senior Resident Engineer (SRE)	Binnies Hong Kong Limited (Binnies)	Mr. Eugene Chan	6392 3809
Independent Environmental Checker (IEC)	Aurecon Hong Kong Limited (Aurecon)	Dr. F.C. Tsang	2698 8060
Environmental Team (ET)	Société Générale de Surveillance (SGS) Hong Kong Limited	Mr. Johnathan Ho	9236 5528
Environmental Officer	China Geo-engineering Corporation (CGC)	Mr. Alex Chow	5918 9179
Hotline Telephone Number			6902 2820

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	D-1
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

APPENDIX D – CONSTRUCTION WORK PROGRAMM

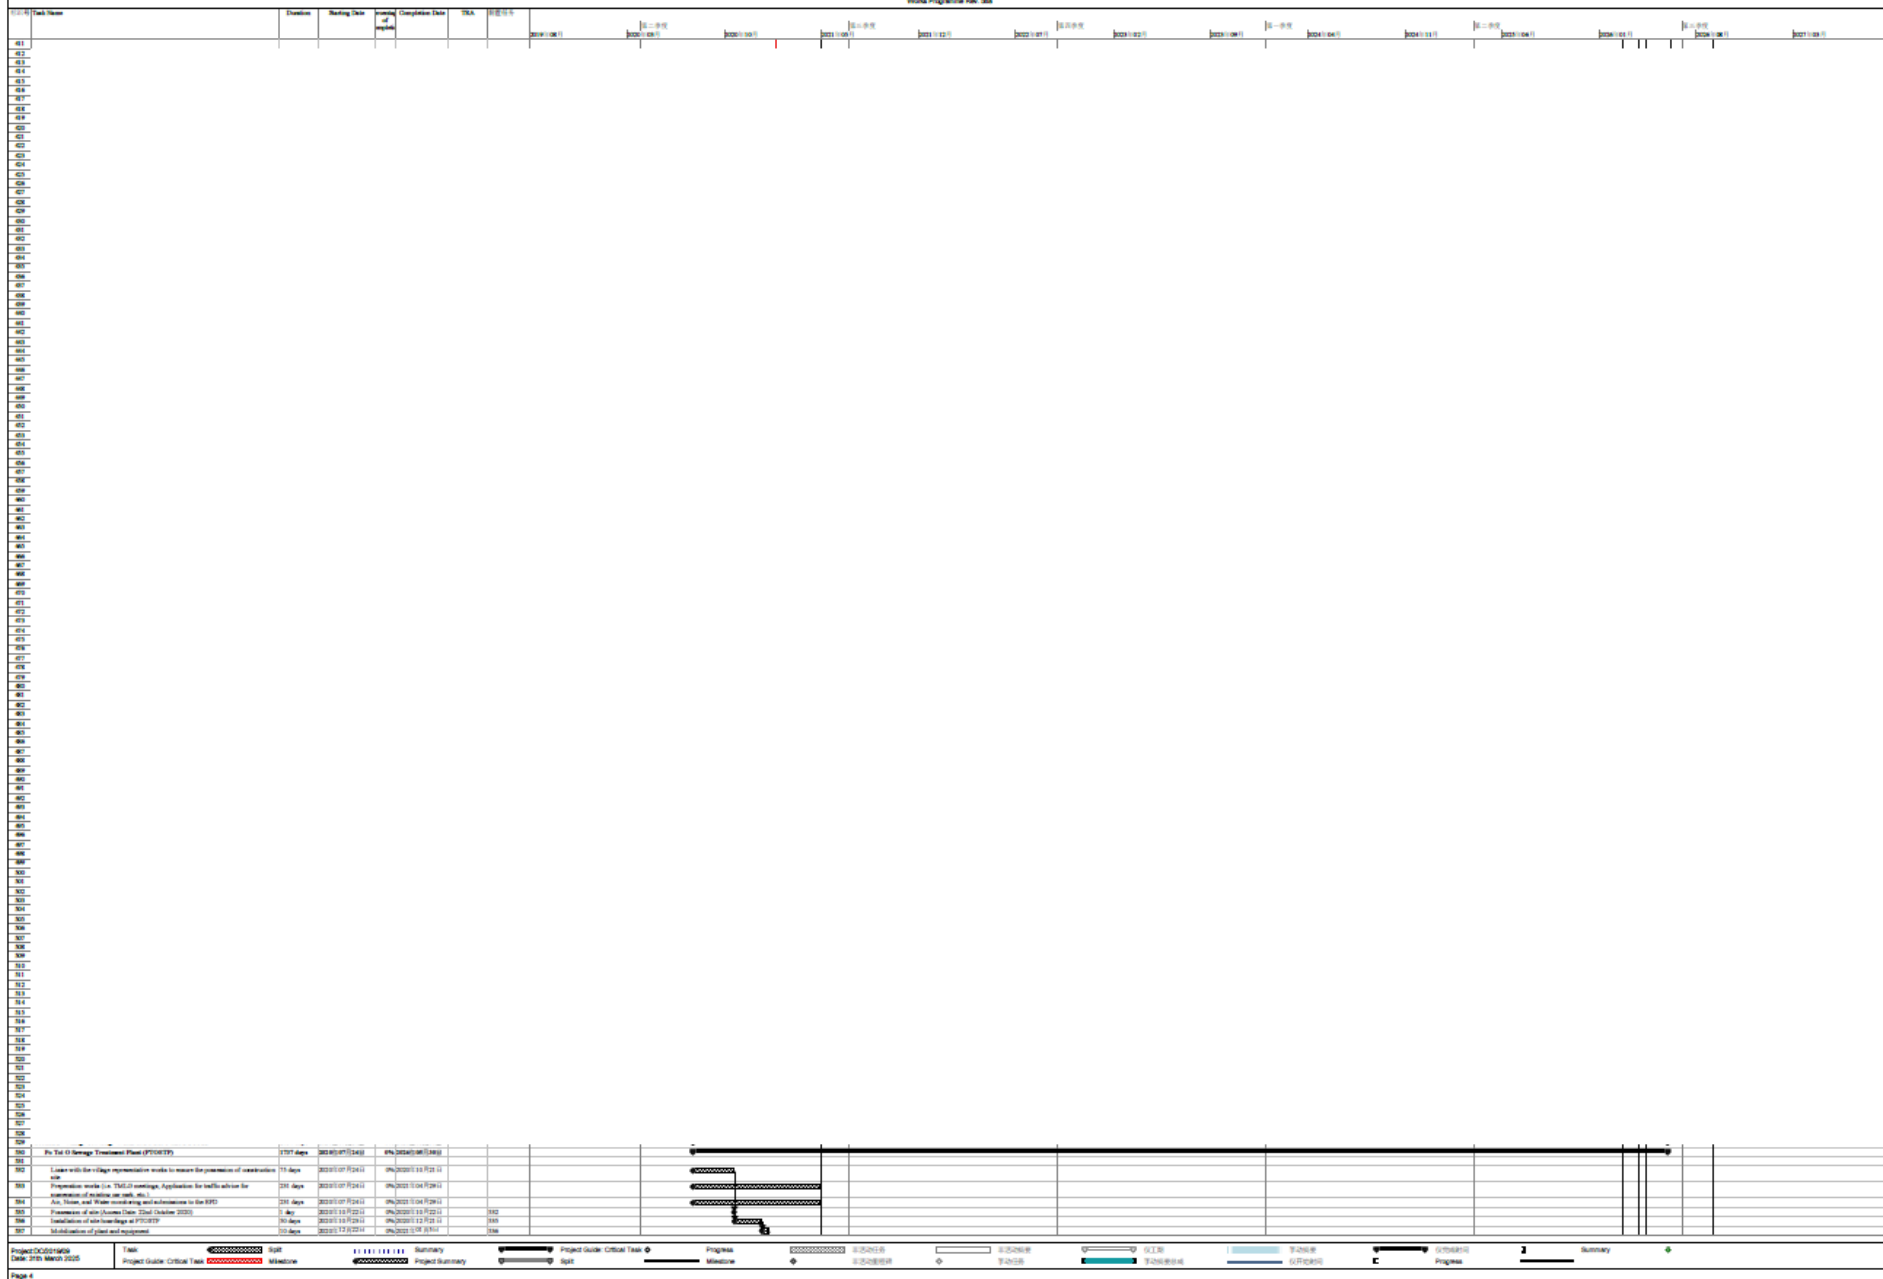

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	E-1
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

APPENDIX E - IMPLETEMENTATION OF RECOMMENDED MITGATION MEASURES

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		Page	E-2
			Ref#	-
	Quarterly EM&A Report		Rev.	01
			Date	Mar 26

Item	EM & A Ref.	EM&A Manual Recommended Mitigation/ Actions	Implementation Status		
			December 2025	January 2026	February 2026
Air Quality Impact	A10	Good housekeeping to minimize dust generation, e.g. by properly handling and storing dusty materials.	✓	✓	✓
	A11	Adopt dust control measures, such as dust suppression using water spray on exposed soil at least 4 times a day, in areas with dusty construction activities and during material handling.	✓	✓	✓
	A12	Store cement bags in shelter with 3 sides and the top covered by impervious materials if the stack exceeds 20 bags.	N/A	N/A	N/A
	A13	Maintain a reasonable height when dropping excavated materials to limit dust generation.	N/A	N/A	N/A
	A14	Limit vehicle speed within construction site and in Po Toi O to 10km/hr and confine vehicle movement in haul road.	✓	✓	✓
	A15	Minimize exposed earth after completion of work in a certain area by hydroseeding, vegetating, soil compacting or covering with bitumen.	✓	✓	✓
	A16	Provide wheel washing at construction site exit to clean the vehicle body and wheel.	✓	✓	✓

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		Page	E-3
			Ref#	-
	Quarterly EM&A Report		Rev.	01
			Date	Mar 26

Item	EM & A Ref.	EM&A Manual Recommended Mitigation/ Actions	Implementation Status		
			December 2025	January 2026	February 2026
Air Quality Impact	A17	Cover materials on trucks before leaving the construction site to prevent debris from dropping during traffic movement or being blown away by wind	✓	✓	✓
	A18	Regular maintenance of plant equipment to prevent black smoke Emission.	✓	✓	✓
	A19	Throttle down or switch off unused machines or machine in intermittent use	✓	✓	✓
	A20	Minimize excavation area as far as possible.	✓	✓	✓
	A21	Store odorous excavated materials in covered containers and remove off-site as soon as possible within 24 hours.	✓	✓	✓
	A22	Cover open stockpiles of construction materials (e.g. aggregates, sand and fill materials) with impermeable materials such as tarpaulin during rainstorms.	✓	✓	✓
	A23	Hoarding of not less than 2.4 m high shall be erected from ground level to surround the construction site for sewage treatment plant along Po Toi O Chuen Road except for a construction site entrance or exit.	N/A	N/A	N/A
	A24	Carry out air quality monitoring throughout the construction period	✓	Rem.	✓

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		Page	E-4
			Ref#	-
	Quarterly EM&A Report		Rev.	01
			Date	Mar 26

Item	EM & A Ref.	EM&A Manual Recommended Mitigation/ Actions	Implementation Status		
			December 2025	January 2026	February 2026
Noise Impact	N1	Use hand-held plant equipment or manual equipment within village area.	✓	✓	✓
	N2	For HDD, enclose the stationary plant equipment on three sides with cover. Only the side facing the sea shall be opened for heat exhaustion.	N/A	N/A	N/A
	N3	Generator should be placed at a fixed location at least 5-6m away from the NSRs and screened by noise barrier whenever excavation work must be carried out at their front doors.	✓	✓	✓
	N4	Avoid carrying out noisy activities at the same time. The work front of village sewer installation near NSRs PTO_N1 and PTO_N3 shall not be conducted concurrently with installation of Po Toi O Chuen Road sewer and horizontal directional drilling respectively.	✓	✓	✓
	N5	Vibratory poker shall only be operated 4m away from NSR and with noise barrier properly erected. Surfacing work within 4m from NSR shall be carried out by manual method.	✓	✓	✓
	N6	Schedule noisy activities to minimize exposure of nearby NSRs to high levels of construction noise.	✓	✓	✓

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		Page	E-5
			Ref#	-
	Quarterly EM&A Report		Rev.	01
			Date	Mar 26

Item	EM & A Ref.	EM&A Manual Recommended Mitigation/ Actions	Implementation Status		
			December 2025	January 2026	February 2026
Noise Impact	N7	Use Quality Powered Mechanical Equipment (QPME) which produces lower noise level.	✓	✓	✓
	N8	Erect 3m high mobile barriers with skid footing and a small cantilevered upper portion within a few meters of stationary plants and within about 5m of more mobile plant.	✓	✓	✓
	N9	Hand-held breaker shall be fitted with mufflers. A movable enclosure made up of plywood is proposed to surround both worker and breaker during breaking process. The internal wall of the enclosure should be laid with sound absorbent such as mineral wool.	✓	✓	✓
	N10	Regular maintenance of plant equipment to prevent noise emission due to impair.	✓	✓	✓
	N11	Position mobile noisy equipment in location and direction away from NSR.	✓	✓	✓
	N12	Use silencer or muffler on plant equipment and should be properly maintained.	✓	✓	✓
	N13	Throttle down or switch off unused machines or machine in intermittent use between work.	✓	✓	✓
	N14	Make good use of stockpiles or other structures for noise screening.	✓	✓	✓

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		Page	E-6
			Ref#	-
	Quarterly EM&A Report		Rev.	01
			Date	Mar 26

Item	EM & A Ref.	EM&A Manual Recommended Mitigation/ Actions	Implementation Status		
			December 2025	January 2026	February 2026
Noise Impact	N15	Mobile plant should be sited as far away from NSRs as possible	✓	✓	✓
	N16	Reduce the percentage on-time for some noisy PMEs	✓	✓	✓
	N17	Carry out noise monitoring	✓	✓	✓

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		Page	E-7
			Ref#	-
	Quarterly EM&A Report		Rev.	01
			Date	Mar 26

Item	EM & A Ref.	EM&A Manual Recommended Mitigation/ Actions	Implementation Status		
			December 2025	January 2026	February 2026
Water Quality Impact	W1	Divert the water from outfall of W3 (stream near Fairway Vista) during open cut excavation for laying of gravity sewer nearby.	✓	✓	✓
	W2	Place sandbag along the upstream section of the stream near Fairway Vista and along rocky shore during open cut excavation for laying of gravity sewers/rising mains nearby.	✓	✓	✓
	W3	Intercept the water from u-channel at the foot of the slope where the STP will be built.	✓	✓	✓
	W4	Install cofferdam around the proposed excavation area for entry pit of HDD work to prevent falling of debris into the sea	N/A	N/A	N/A
	W5	Install sheet piles in Junine waters by vibratory action.	N/A	N/A	N/A
	W6	Junine works (dredging, construction and installation works at diffuser location, backfilling) shall be carried out inside the watertight cofferdam. The cofferdam can only be removed after completion of work.	N/A	N/A	N/A
	W7	Dredging should be carried out by grab dredgers anchored outside the cofferdam. The Junine sediment should be placed in sealed compartment of the Junine barge.	N/A	N/A	N/A
	W8	Water removed from the cofferdam should be desilted before discharge back into the sea.	N/A	N/A	N/A

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		Page	E-8
			Ref#	-
	Quarterly EM&A Report		Rev.	01
			Date	Mar 26

Item	EM & A Ref.	EM&A Manual Recommended Mitigation/ Actions	Implementation Status		
			December 2025	January 2026	February 2026
Water Quality Impact	W9	Carry out water quality monitoring at water sensitive receivers before and during cofferdam installation works, throughout dredging works, and during cofferdam extraction works.	N/A	N/A	N/A
	W12	Set up sedimentation tank for settling suspended solids in wastewater before discharge into storm drains. Sand/silt removal facilities such as sand traps, silt traps and sedimentation basin should be provided with adequate capacity.	✓	✓	Rem.
	W13	Follow ProPECC PN 1/94 "Construction Site Drainage" as far as practicable	✓	✓	✓
	W14	Construct catchpits and perimeter channels prior to commencement of site formation works and earthworks	✓	✓	✓
	W15	Maintain silt removal facilities, channels, manholes before and after rainstorm.	✓	✓	✓
	W16	Remove silt and grit from silt trap at regular interval.	✓	✓	✓
	W17	Well design works program to minimize the work areas to minimize the soil exposure and site runoff.	✓	✓	✓

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		Page	E-9
			Ref#	-
	Quarterly EM&A Report		Rev.	01
			Date	Mar 26

Item	EM & A Ref.	EM&A Manual Recommended Mitigation/ Actions	Implementation Status		
			December 2025	January 2026	February 2026
Water Quality Impact	W18	Arrange soil excavation works outside rainy seasons (April to December) as far as possible. If this cannot be achieved, the following measures should be implemented:	✓	✓	✓
		Cover temporary exposed slope surfaces with impermeable materials, e.g. tarpaulin.	✓	✓	✓
		Protect temporary access roads by crushed stone or gravel.	✓	✓	✓
		Provide intercepting channels along crest/edge of excavation.	✓	✓	✓
	W19	Minimize exposed earth after completion of work in a certain area by hydroseeding, vegetating, soil compacting or covering with bitumen.	✓	✓	✓
	W20	Prevent rainwater from entering trenches. Excavation of trenches should be dug and backfilled in short sections during rainy seasons. Remove silt in rainwater collected from the trenches or foundation excavations prior to discharge to storm drains.	✓	✓	✓

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		Page	E-10
			Ref#	-
	Quarterly EM&A Report		Rev.	01
			Date	Mar 26

Item	EM & A Ref.	EM&A Manual Recommended Mitigation/ Actions	Implementation Status		
			December 2025	January 2026	February 2026
Water Quality Impact	W21	Cover open stockpiles of construction materials (e.g. aggregates, sand and fill materials) with impermeable materials such as tarpaulin during rainstorms.	✓	✓	✓
	W22	Cover and temporary seal manholes to prevent silt, construction materials or debris and surface runoff from entering foul sewers.	✓	✓	✓
	W23	Remove waste from the construction site regularly.	✓	✓	✓
	W24	Apply discharge license for effluent discharge. Treat the discharge to comply with the requirement in TM-DSS.	✓	✓	✓
	W25	Reuse treated effluent onsite, e.g. dust suppression, wheel washing and general cleaning.	✓	✓	✓
	W26	Monitor effluent water quality.	✓	✓	✓
	W27	Register as chemical waste producer if chemical waste will be generated.	✓	✓	✓
	W28	Perform maintenance of vehicles and equipment that have oil leakage and spillage potential on hard standings within a bunded area with sumps and oil interceptors.	✓	✓	✓

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	E-11
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

Item	EM & A Ref.	EM&A Manual Recommended Mitigation/ Actions	Implementation Status		
			December 2025	January 2026	February 2026
Water Quality Impact	W29	Dispose chemical waste in accordance to Waste Disposal Ordinance. Follow the <i>Code of Practice on the Packaging, Labelling and Storage of Chemical Wastes</i> , examples as follows:	✓	✓	✓
		Store chemical wastes with suitable containers to avoid leakage or spillage during storage, handling and transport.	✓	✓	✓
		Label chemical waste containers according to the CoP to notify and warn the waste handlers.	✓	✓	✓
		Store chemical wastes at designated safe location with adequate space.	✓	✓	✓
	W30	Provide sufficient chemical toilets with regular maintenance by registered waste collector where necessary.	✓	✓	✓
	W31	Provide a drip tray/container underneath the bentonite recycling system.	N/A	N/A	N/A
	W32	Carry out regular site inspection to audit the implementation of mitigation measures.	✓	✓	✓
	W33	Carry out effluent quality monitoring at location specified in the discharge license.	✓	✓	✓

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		Page	E-12
			Ref#	-
	Quarterly EM&A Report		Rev.	01
			Date	Mar 26

Item	EM & A Ref.	EM&A Manual Recommended Mitigation/ Actions	Implementation Status		
			December 2025	January 2026	February 2026
Waste/Chemical Management	WM4	Allocate an area for waste sorting and storage of C&D materials into the following categories for reuse, recycle or disposal if possible. Remove waste from the construction site for sorting once generated if no suitable space can be identified.	✓	✓	✓
		Excavated materials suitable for reuse	✓	✓	✓
		Inert C&D materials (or public fill) for disposal offsite	✓	✓	✓
		Non-inert C&D materials (or C&D waste) for disposal at landfills	✓	✓	✓
		Records of quantities generated/ recycled/ disposed maintained?	✓	✓	✓
		Chemical waste	✓	✓	✓
		Bentonite slurry for reconditioning and reuse	N/A	N/A	N/A
		General refuse	✓	✓	✓

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		Page	E-13
			Ref#	-
	Quarterly EM&A Report		Rev.	01
			Date	Mar 26

Item	EM & A Ref.	EM&A Manual Recommended Mitigation/ Actions	Implementation Status		
			December 2025	January 2026	February 2026
Waste/Chemical Management	WM5	Adopt good site practice as follows:	✓	✓	✓
		Provide training to workers on site cleanliness, waste management (waste reduction, reuse and recycle) and chemical handling procedures.	✓	✓	✓
		Cover waste materials with tarpaulin or in enclosure during transportation.	✓	✓	✓
		Maintain drainage systems, sumps and oil interceptors.	✓	✓	✓
		Sort out chemical waste for proper handling and treatment onsite or offsite.	✓	✓	✓

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		Page	E-14
			Ref#	-
	Quarterly EM&A Report		Rev.	01
			Date	Mar 26

Item	EM & A Ref.	EM&A Manual Recommended Mitigation/ Actions	Implementation Status		
			December 2025	January 2026	February 2026
Waste/Chemical Management	WM6	Adopt good site practice as follows:	✓	✓	✓
		Allocate area/containers for sorting, recovering and storing waste for reuse, recycle or disposal (e.g. demolition debris and excavated materials, general refuse like aluminum cans.) Remove waste from the construction site for sorting once generated if no suitable space can be identified.	✓	✓	✓
		Allocate area for proper storage of construction materials to prevent contamination prevent soil contamination?	✓	✓	✓
		Maintain drainage systems, sumps and oil interceptors.	✓	✓	✓
		Minimize wastage through careful planning and avoiding over purchase of construction materials	✓	✓	✓

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		Page	E-15
			Ref#	-
	Quarterly EM&A Report		Rev.	01
			Date	Mar 26

Item	EM & A Ref.	EM&A Manual Recommended Mitigation/ Actions	Implementation Status		
			December 2025	January 2026	February 2026
Waste/Chemical Management	WM7	Prepare and implement a site-specific Waste Management Plan (WMP) as part of Environmental Management Plan (EMP) in accordance with ETWB TCW No. 19/2005. Detail waste management method in the form of avoidance, reuse, recovery, recycling, storage, collection, treatment and disposal according to the recommendations on the EIA and EM&A Manual. It should be approved by the ER and regularly reviewed.	✓	✓	✓
	WM8	Store waste materials properly as follows:	✓	✓	✓
		Avoid contamination by proper handling and storing waste.	✓	✓	✓
		Prevent erosion by covering waste.	✓	✓	✓
		Apply water spray on excavated materials.	✓	✓	✓
		Maintain and clean storage area regularly.	✓	✓	✓
		Sort and stockpile different materials at designated location to enhance reuse.	✓	✓	✓

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		Page	E-16
			Ref#	-
	Quarterly EM&A Report		Rev.	01
			Date	Mar 26

Item	EM & A Ref.	EM&A Manual Recommended Mitigation/ Actions	Implementation Status		
			December 2025	January 2026	February 2026
Waste/Chemical Management	WM9	Apply for relevant waste disposal permits in accordance with the Waste Disposal Ordinance (Cap. 354), Waste Disposal (Charges for Disposal of Construction Waste) Regulation (Cap. 345) and the Land (Miscellaneous Provisions) Ordinance (Cap.28) Dumping at Sea Ordinance (Cap. 466).	✓	✓	✓
	WM10	Hire licensed waste disposal contractors for waste collection and removal. Dispose waste at licensed waste disposal facilities	✓	✓	✓
	WM11	Implement trip-ticket system for recording the amount of waste generated, recycled and disposed, including chemical wastes	✓	✓	✓
	WM12	Provide wheel washing at construction site exit to clean the vehicle body and wheel.	✓	✓	✓
	WM13	Reduce water content in wet spoil generated from piling work by mixing with dry materials. Only dispose treated spoil with less than 25% dry density to Public Fill Reception Facilities	✓	✓	✓

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		Page	E-17
			Ref#	-
	Quarterly EM&A Report		Rev.	01
			Date	Mar 26

Item	EM & A Ref.	EM&A Manual Recommended Mitigation/ Actions	Implementation Status		
			December 2025	January 2026	February 2026
Waste/Chemical Management	WM14	Dispose dry waste or waste with less than 70% water content by weight to landfill.	✓	✓	✓
	WM15	Follow the Code of Practice on the Packaging, Labelling and Storage of Chemical Waste as follows:	✓	✓	✓
		Store chemical wastes with suitable containers. Seal and maintain the container to avoid leakage or spillage during storage, handling and transport.	✓	✓	✓
		Label chemical waste containers in both English and Chinese with instructions in accordance to Schedule 2 of the Waste Disposal (Chemical Waste) (General) Regulation.	✓	✓	✓
		The container capacity should be smaller than 450 litres unless agreed by the EPD.	✓	✓	✓

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		Page	E-18
			Ref#	-
	Quarterly EM&A Report		Rev.	01
			Date	Mar 26

Item	EM & A Ref.	EM&A Manual Recommended Mitigation/ Actions	Implementation Status		
			December 2025	January 2026	February 2026
Waste/Chemical Management	WM16	Comply with the requirement of the chemical storage area:	✓	✓	✓
		Store only chemical waste and label clearly the chemical characters of the waste.	✓	✓	✓
		Have at least 3 sides enclosed and protected from rainfall with cover.	✓	✓	✓
		Provide sufficient ventilation	✓	✓	✓
		Have impermeable floor and has bunds to contain 110% of the capacity of the largest container or 20% of the total volume of the stored waste in the area, whichever is larger		✓	✓
	WM17	Transfer used lubricants, waste oils and other chemicals to oil recycling companies, if possible, and empty oil drums for reuse or refill. No direct or indirect discharge is permitted	✓	✓	✓
	WM18	Hire licensed chemical waste disposal contractors for waste collection and removal. Dispose chemical waste at the approved Chemical Waste Treatment Centre at Tsing Yi or other licensed facility.	✓	✓	✓
	WM19	Hire reputable waste collector to Separately collect and dispose general refuse from other wastes. Cover the waste to prevent being blown away.	✓	✓	✓

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		Page	E-19
			Ref#	-
	Quarterly EM&A Report		Rev.	01
			Date	Mar 26

Item	EM & A Ref.	EM&A Manual Recommended Mitigation/ Actions	Implementation Status		
			December 2025	January 2026	February 2026
Waste/Chemical Management	WM20	Provide recycling bins for sorting out recyclables for collection by recycling companies. Non-recyclables should be removed to designated landfills every day by licensed collectors to prevent environmental and health nuisance.	✓	✓	✓
	WM21	Organize training and reminders to site staff on waste minimization through avoidance and reduction, reusing and recycling.	✓	✓	✓
	WM22	Used bentonite shall be reconditioned onsite and reused as far as practical to minimize wastage. If this is deemed not viable, the used bentonite shall be delivered offsite for reconditioning.	N/A	N/A	N/A
	WM23	Characterize the sediment quality of the Marine sediment to be dredged and submit a Sediment Quality Report for EPD's approval. Dispose the dredged Marine sediment in accordance with ETWB TC(W) No. 34/2002.	N/A	N/A	N/A

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		Page	E-20
			Ref#	-
	Quarterly EM&A Report		Rev.	01
			Date	Mar 26

Item	EM & A Ref.	EM&A Manual Recommended Mitigation/ Actions	Implementation Status		
			December 2025	January 2026	February 2026
Ecology	E1	Erect bright colour fencing along the boundary of the undisturbed region of the shrubland and woodland, and around <i>Diospyros vaccinioides</i> , a plant species of conservation importance, near the work boundary to remind workers not to trespass or occupy the area, and to be careful during operation of equipment.	✓	✓	✓
	E2	Reinstate the disturbed rocky shore with the rocks temporarily removed.	N/A	N/A	N/A
	E3	Place sandbag around the section of W3 next to Fairway Vista and along the shore during open cut excavation for laying of gravity sewer nearby.	✓	✓	✓
	E4	Temporarily divert the water from outfall of W3 away from excavation area.	✓	✓	✓
	E5	Inspect the condition of the <i>Diospyros vaccinioides</i> near the work boundary as part of weekly site audit.	✓	✓	✓
	E6	Erection of hoarding, fencing or provision of clear deJunctionation of work zones	✓	✓	✓

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		Page	E-21
			Ref#	-
	Quarterly EM&A Report		Rev.	01
			Date	Mar 26

Item	EM & A Ref.	EM&A Manual Recommended Mitigation/ Actions	Implementation Status		
			December 2025	January 2026	February 2026
Ecology	E7	Designate areas for placement of equipment, building materials and wastes away from the natural environment.	✓	✓	✓
	E8	Carry out tree preservation and compensatory tree planting will be carried out in accordance with DEVB TCW No. 7/2015.	✓	✓	✓

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		Page	E-22
			Ref#	-
	Quarterly EM&A Report		Rev.	01
			Date	Mar 26

Item	EM & A Ref.	EM&A Manual Recommended Mitigation/ Actions	Implementation Status		
			December 2025	January 2026	February 2026
Landscape and Visual	CM8	Protective materials to be provided to natural rocky coastline to prevent damage to existing landform from plant and machinery during temporary drilling operations. Reinstatement following removal of plant & equipment to original or improved condition shall be undertaken.	N/A	N/A	N/A
	OM2	Use of appropriate building materials and colours for Sewage Treatment Plant to complement surroundings	N/A	N/A	N/A
	CM1	The construction area and contractor's temporary works areas should be minimized to avoid impacts on adjacent landscape. All slope excavation shall take place from within the work boundary to minimize impacts on adjacent slopes.	✓	✓	✓
	CM2	Reduction of construction period to practical minimum.	✓	✓	✓
	CM3	Construction traffic (land and sea) including construction plant, construction vessels and barges to be kept to a practical minimum.	✓	✓	✓
	CM4	Erection of decorative mesh screens or construction hoardings and/or temporary noise barriers around works areas in visually unobtrusive colors.	✓	✓	✓
	CM5	Avoidance of excessive height and bulk of site buildings and structures.	✓	✓	✓

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		Page	E-23
			Ref#	-
	Quarterly EM&A Report		Rev.	01
			Date	Mar 26

Item	EM & A Ref.	EM&A Manual Recommended Mitigation/ Actions	Implementation Status		
			December 2025	January 2026	February 2026
Landscape and Visual	CM6	Protective materials to be provided to natural rocky coastline to prevent damage to existing landform from plant and machinery during temporary drilling operations. Reinstatement following removal of plant & equipment to original or improved condition shall be undertaken.	✓	✓	✓
	CM7	All existing trees shall be carefully protected during construction. A Detailed Tree Protection Specification shall be provided in the Contract Specification. Under this specification, the Contractor shall be required to submit, for approval, a detailed working method statement for the protection of trees prior to undertaking any works adjacent to all retained trees, including trees in contractor's works areas. Tree risk assessment shall be undertaken to all existing trees within the project site as per "Guidelines for Tree Risk Assessment and Management Arrangement"	✓	✓	✓
	OM3	Lighting units to be directional and minimize unnecessary light spill and glare.	N/A	N/A	N/A
	OM4	Greening measures to reinstate the landscape which are appropriate to the context, including tree and shrub planting and vertical greening, shall be implemented.	N/A	N/A	N/A

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		Page	E-24
			Ref#	-
	Quarterly EM&A Report		Rev.	01
			Date	Mar 26

Item	EM & A Ref.	EM&A Manual Recommended Mitigation/ Actions	Implementation Status		
			December 2025	January 2026	February 2026
Building Heritage	BH1	Undertake condition survey by professional qualified building surveyor or engineer to record the existing condition of the built heritage resources.	✓	✓	✓
	BH2	Carry out vibration and settlement monitoring to build heritage resources. A maximum vibration level 7.5mm/s shall be adopted for the Grade 3 Hung Shing Temple and settlement check points in the Alert/Alarm/Action limit levels at 6mm/8mm/10mm shall be adopted.	✓	✓	✓
	BH3	Are protective covering or protective screen provided to build heritage resources which are close to building area? (c.f. BH3)	N/A	N/A	N/A
	BH4	Maintain public access to the cultural landscape features (c.f. BH4)	N/A	N/A	N/A
	BH5	Provision of at least 1m buffer zone from the proposed works provided? (c.f. BH5)	N/A	N/A	N/A

Remark

N/A – Not Applicable

✓ – Implemented

Obs. – Observed

Rem. – Reminder

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	F-1
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

APPENDIX F - METEOROLOGICAL DATA EXTRACTED FROM HONG KONG OBSERVATORY

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O							Page	F-2
								Ref#	-
	Quarterly EM&A Report							Rev.	01
								Date	Mar 26

2025/12 Daily Extract of Meteorological Observations from HKO

Day	Hong Kong Observatory								King's Park	Waglan Island [^]	
	Mean Pressure (hPa)	Air Temperature			Mean Dew Point (deg. C)	Mean Relative Humidity (%)	Mean Amount of Cloud (%)	Total Rainfall (mm)	Total Bright Sunshine (hours)	Prevailing Wind Direction (degrees)	Mean Wind Speed (km/h)
		Absolute Daily Max (deg. C)	Mean (deg. C)	Absolute Daily Min (deg. C)							
1	1014.4	25.6	22.9	21	19	79	74	1.3	***	***	***
2	1014.9	24.5	22.8	21.7	18.3	76	83	Trace	***	***	***
3	1019.4	22.7	21.5	20.5	15.3	69	89	2	***	***	***
4	1021.4	20.9	19.8	18.9	14.6	72	76	0	***	***	***
5	1021.3	22.8	20.4	18.9	15.2	72	45	0	***	***	***
6	1019.8	22.9	20.4	18.8	15.6	74	27	0	***	***	***
7	1019.5	24	21.3	18.7	15.8	72	67	0	***	***	***
8	1019.3	25.5	22.5	20.5	13.9	59	30	0	***	***	***
9	1019.8	23.4	21.1	19.5	14.8	68	32	0	***	***	***
10	1018.8	21.9	20.8	19.7	17.1	79	89	0.2	***	***	***
11	1017.8	26	22.7	20.4	16.8	70	69	0	***	***	***
12	1018.3	21.8	21.1	20.3	15.5	71	56	0	***	***	***
13	1019.8	22.6	20	15.7	14.7	72	88	0.7	***	***	***
14	1021.9	19.5	17	15.6	5.5	48	81	Trace	***	***	***
15	1021.4	19.9	17.6	15.6	8.4	56	23	0	***	***	***
16	1019.7	22.9	20.1	18	14.2	69	34	0	***	***	***
17	1019.7	25.3	21.4	18.3	15.4	70	12	0	***	***	***
18	1019.4	22.4	20.4	19.1	15.4	73	52	0	***	***	***
19	1016.6	23.7	21	18.9	16.6	76	81	0.3	***	***	***
20	1016.6	24.9	23	21.2	15.7	64	65	0	***	***	***
21	1018.2	24.7	21.9	19.9	17	74	41	0	***	***	***
22	1018.9	21	19.7	19	14.9	74	76	0	***	***	***
23	1017.2	21.3	20	18.9	15.2	74	73	0.3	***	***	***
24	1014.6	23.8	21.3	19.1	17.2	78	55	0	***	***	***
25	1018.3	20.8	17.8	14.8	11.1	66	77	1.7	***	***	***
26	1021.2	15.5	14.7	14	7.3	61	91	0	***	***	***
27	1020.1	19.5	16.8	13.8	10.3	66	44	0	***	***	***
28	1019	20.5	18	16.1	12.6	71	35	0	***	***	***
29	1016.9	21.5	18.8	16.8	14.1	75	20	0	***	***	***
30	1015.4	23.3	19.5	17.1	14.5	73	32	0	***	***	***
31	1014.8	20.8	19.4	18.6	14.2	72	77	0	***	***	***
Mean/Total	1018.5	22.4	20.2	18.4	14.4	70	58	6.5	***	***	***
Climatologic al Normal?	1020.1	20.4	18.2	16.2	12.4	70	57	28.8	161.6	10	26.4

[^] Information of wind direction and wind speed for Waglan Island are based on automatic weather station data since February 1989

Trace means rainfall less than 0.05 mm

? 1991-2020 Climatological Normal, unless otherwise specified

Source: [Daily Extract | Hong Kong Observatory\(HKO\) | Climate Information Service](#)

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		Page	F-3
			Ref#	-
	Quarterly EM&A Report		Rev.	01
			Date	Mar 26

2026/01 Daily Extract of Meteorological Observations from HKO

Day	Hong Kong Observatory								King's Park	Waglan Island [^]	
	Mean Pressure (hPa)	Air Temperature			Mean Dew Point (deg. C)	Mean Relative Humidity (%)	Mean Amount of Cloud (%)	Total Rainfall (mm)	Total Bright Sunshine (hours)	Prevailing Wind Direction (degrees)	Mean Wind Speed (km/h)
		Absolute Daily Max (deg. C)	Mean (deg. C)	Absolute Daily Min (deg. C)							
1	1017.9	21.7	18.8	16.5	12.9	69	43	0	***	***	***
2	1023.5	17.7	15	12.8	5.8	55	24	0	***	***	***
3	1024.7	16.5	14.3	11.4	6.5	60	18	0	***	***	***
4	1022.2	20.3	17	14.1	10.5	65	32	0	***	***	***
5	1020.9	22.1	18.3	15.1	10.8	63	6	0	***	***	***
6	1024.3	16.8	14	11.8	3.5	50	18	0	***	***	***
7	1025.3	16.4	13.4	10.9	-0.2	39	2	0	***	***	***
8	1024.9	18.1	14.9	11.8	-1.7	33	1	0	***	***	***
9	1022.8	18.9	15.7	13	2.3	42	12	0	***	***	***
10	1020.8	20.6	17.1	14.2	7.3	54	14	0	***	***	***
11	1023.1	20.7	17.5	14.7	3.4	41	2	0	***	***	***
12	1021.4	20.6	17.5	15.7	11.1	67	41	0	***	***	***
13	1018.7	22.5	18.9	15.9	10.8	61	6	0	***	***	***
14	1018.3	21.2	18.8	17	10.6	59	9	0	***	***	***
15	1016.5	23.1	19.2	16.2	13.7	72	22	1	***	***	***
16	1014.3	24	19.9	16.9	12	62	6	0	***	***	***
17	1013	24.8	20.7	17.6	10.6	54	7	0	***	***	***
18	1013.3	22.4	20.2	18.9	11.1	57	9	0	***	***	***
19	1014.8	21.9	19.6	18.1	15.2	76	20	0	***	***	***
20	1018.1	20.1	18.6	17.6	13.3	71	75	0	***	***	***
21	1021.8	18.1	15.7	14.9	8.7	63	90	0	***	***	***
22	1024.3	16.3	14.2	12.9	7.1	63	88	0	***	***	***
23	1024.6	17.5	14.5	12.3	7.8	64	87	0	***	***	***
24	1022.5	19.6	16.8	14.7	11.2	69	44	0	***	***	***
25	1020.9	20.1	18.2	16.6	13.4	74	63	0	***	***	***
26	1020.2	22.6	19.7	17.8	15.7	78	80	0	***	***	***
27	1019.6	24.8	21.1	18.9	16.7	76	72	Trace	***	***	***
28	1021.2	21.3	18.8	17.9	14.6	77	71	Trace	***	***	***
29	1020.8	19.9	18.2	16.8	12.6	70	78	0	***	***	***
30	1020.1	20.4	19.2	17.6	14.7	75	92	Trace	***	***	***
31	1020.8	19.6	18.2	16	15.5	85	97	2.2	***	***	***
Mean/Total	1020.5	20.3	17.5	15.4	9.9	63	40	3.2	***	***	***
Climatologic al Normal?	1020.1	18.7	16.5	14.6	11.7	74	62	33.2	145.8	60	25.1

[^] Information of wind direction and wind speed for Waglan Island are based on automatic weather station data since February 1989

Trace means rainfall less than 0.05 mm

? 1991-2020 Climatological Normal, unless otherwise specified

Source: [Daily Extract | Hong Kong Observatory\(HKO\) | Climate Information Service](#)

2026/02 Daily Extract of Meteorological Observations from HKO

Day	Hong Kong Observatory								King's Park	Waglan Island^	
	Mean Pressure (hPa)	Air Temperature			Mean Dew Point (deg. C)	Mean Relative Humidity (%)	Mean Amount of Cloud (%)	Total Rainfall (mm)	Total Bright Sunshine (hours)	Prevailing Wind Direction (degrees)	Mean Wind Speed (km/h)
		Absolute Daily Max (deg. C)	Mean (deg. C)	Absolute Daily Min (deg. C)							
1	1023.4	19.7	15.8	12	11.5	76	92	1.6	4.2	***	***
2	1024	21	17.5	15.2	11	66	34	0	9.2	***	***
3	1024.1	20.2	17.8	16.5	12.9	73	83	0	3	***	***
4	1019.9	22.1	18.8	16.6	13.7	73	54	0	8.3	***	***
5	1016.7	25.2	20.9	18.1	16.8	78	47	0	8.1	***	***
6	1015.2	26.2	22.1	18.9	16.5	72	19	0	9	***	***
7	1018.7	21.2	19.6	18.3	16.2	81	77	Trace	1.5	***	***
8	1024.3	18.4	16.5	14.9	9	62	81	0.1	0.9	***	***
9	1022.7	16.4	15.5	14.1	9.2	66	79	0	2	***	***
10	1020.7	19.6	17.9	16.4	13.6	76	83	0	1.5	***	***
11	1020.6	25.2	21	18	15.7	73	45	0	10	***	***
12	1020.2	19.9	18.4	17.6	14.5	78	78	0	1.2	***	***
13	1017.7	24.5	20.2	17.7	14.7	71	35	0	10.5	***	***
14	1016.2	25.8	21.8	18.5	17.1	76	25	0	10.4	***	***
15	1015.7	26.9	22.9	20.9	19.5	81	48	0	6.8	***	***
16	1015.3	27.9	24	22	20.1	79	52	0	8.8	***	***
17	1019.3	22.4	19.5	18.2	15.8	80	91	Trace	0	***	***
18	1021.9	23	19.6	17.9	12.8	65	58	Trace	8.4	***	***
19	1022.3	22.4	19.6	17.8	13.9	70	59	Trace	9.5	***	***
20	1018.7	24.6	20.9	18.6	15.4	72	33	0	10.4	***	***
21	1013.5	23.4	21	19.2	17.2	79	44	0	8.4	***	***
22	1012.5	25.3	22.3	20.2	17.6	76	51	0	6.5	***	***
23	1013.6	23	21.4	20.8	17.5	79	67	0	6	***	***
24	1013.7	25.7	22.3	19.5	19.1	83	83	0.4	2.9	***	***
25	1014.3	26	22.7	21.3	19.3	81	79	Trace	7	***	***
26	1012.3	21.9	20.5	19	17.7	84	92	0.2	1.3	***	***
27	1010.1	22.8	21.4	20.4	19.4	88	88	0.3	0.3	***	***
28	1010.8	21.8	20	19	18.7	93	90	39	0	***	***
Mean/Total	1017.8	22.9	20.1	18.1	15.6	76	63	41.6	156.1	***	***
Climatological Normal?	1018.7	19.4	17.1	15.3	13.2	79	72	38.9	101.7	60	24.2

^ Information of wind direction and wind speed for Waglan Island are based on automatic weather station data since February 1989

Trace means rainfall less than 0.05 mm

? 1991-2020 Climatological Normal, unless otherwise specified

Source: [Daily Extract | Hong Kong Observatory\(HKO\) | Climate Information Service](#)

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	G-1
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

APPENDIX G - GRAPHICAL PLOTS OF THE MONITORING RESULT

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	G-2
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

AMS1N – 1-hour and 24-hour TSP monitoring

Date	Weather	1-hour TSP Monitoring	24-hour TSP monitoring
		Average Concentration (µg/m3)	Average Concentration (µg/m3)
4- Dec -25	Cloudy	37.0	39.0
10- Dec -25	Cloudy	49.0	32.0
16- Dec -25	Fine	41.3	41.0
22- Dec -25	Fine	59.0	45.0
27- Dec -25	Fine	46.7	45.0

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	G-3
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26


Date	Weather	1-hour TSP Monitoring	24-hour TSP monitoring
		Average Concentration (µg/m3)	Average Concentration (µg/m3)
2- Jan -26	Sunny	47.3	46.0
8- Jan -26	Fine	33.7	34.0
14- Jan -26	Fine	41.0	25.0
19- Jan -26	Sunny	35.0	33.0
23- Jan -26	Cloudy	38.7	39.0
28- Jan -26	Fine	84.0	57.0

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	G-4
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

Date	Weather	1-hour TSP Monitoring	24-hour TSP Monitoring
		Average Concentration (µg/m3)	Average Concentration (µg/m3)
3- Feb -26	Sunny	41.7	47.0
9- Feb -26	Sunny	39.0	38.0
14- Feb -26	Fine	35.3	34.0
20- Feb -26	Sunny	35.0	31.0
26- Feb -26	Cloudy	34.0	32.0
	Average:	43.6	38.6
	Action Level:	319	153
	Limit Level:	500	260


	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	G-6
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

AMS1N- 1 – hour TSP Monitoring

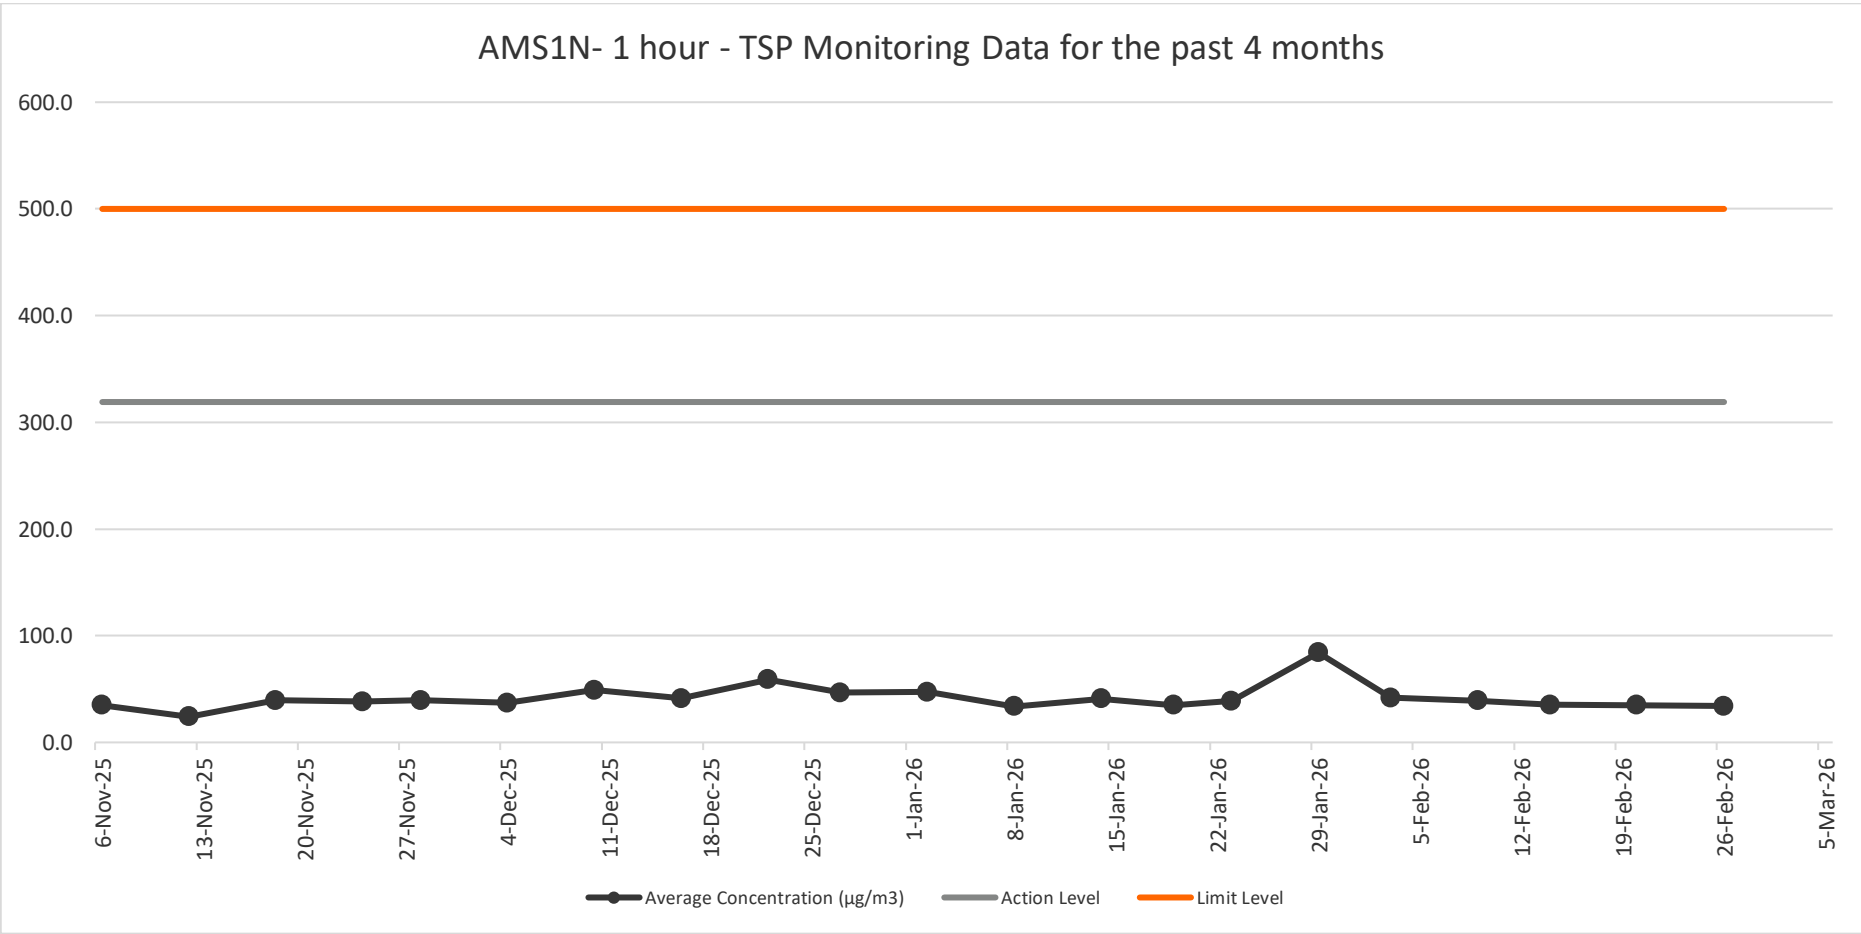

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	G-7
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

AMS1N- 24– hour TSP Monitoring

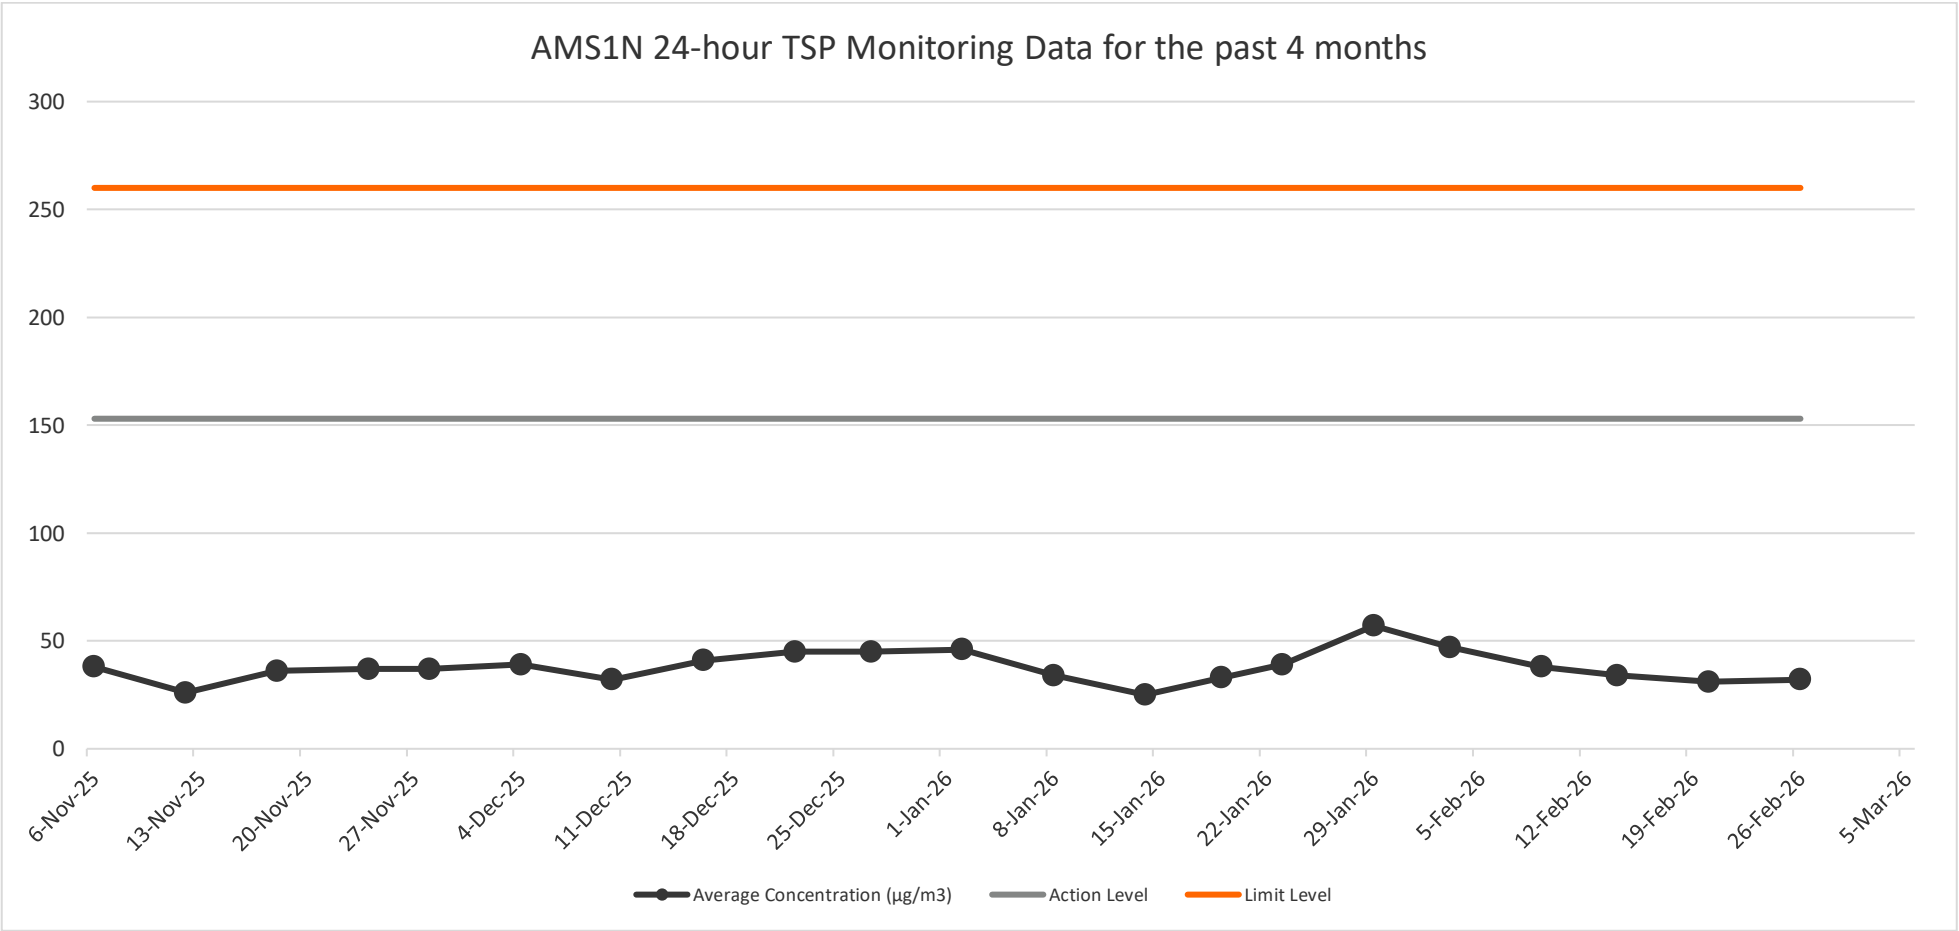

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	G-8
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

AMS2N1 – 1- hour and 24-hour TSP Monitoring

Date	Weather	1-hour TSP Monitoring	24-hour TSP monitoring
		Average Concentration (µg/m3)	Average Concentration (µg/m3)
4- Dec -25	Cloudy	37.3	37.0
10- Dec -25	Cloudy	32.0	35.0
16- Dec -25	Fine	42.7	47.0
22- Dec -25	Fine	61.3	45.0
27- Dec -25	Fine	44.7	41.0

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	G-8
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26


Date	Weather	1-hour TSP Monitoring	24-hour TSP monitoring
		Average Concentration (µg/m3)	Average Concentration (µg/m3)
2- Jan -26	Sunny	33.0	34.0
8- Jan -26	Fine	37.0	31.0
14- Jan -26	Fine	33.3	21.0
19- Jan -26	Sunny	39.0	38.0
23- Jan -26	Cloudy	32.7	31.0
28- Jan -26	Fine	69.0	52.0

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	G-9
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

Date	Weather	1-hour TSP Monitoring	24-hour TSP Monitoring
		Average Concentration (µg/m3)	Average Concentration (µg/m3)
3- Feb -26	Sunny	40.7	39.0
9- Feb -26	Sunny	41.0	40.0
14- Feb -26	Fine	31.3	30.0
20- Feb -26	Sunny	39.0	39.0
26- Feb -26	Cloudy	36.7	40.0
	Average:	40.7	37.5
	Action Level:	279	179
	Limit Level:	500	260


	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	G-10
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

AMS2N- 1 – hour TSP Monitoring

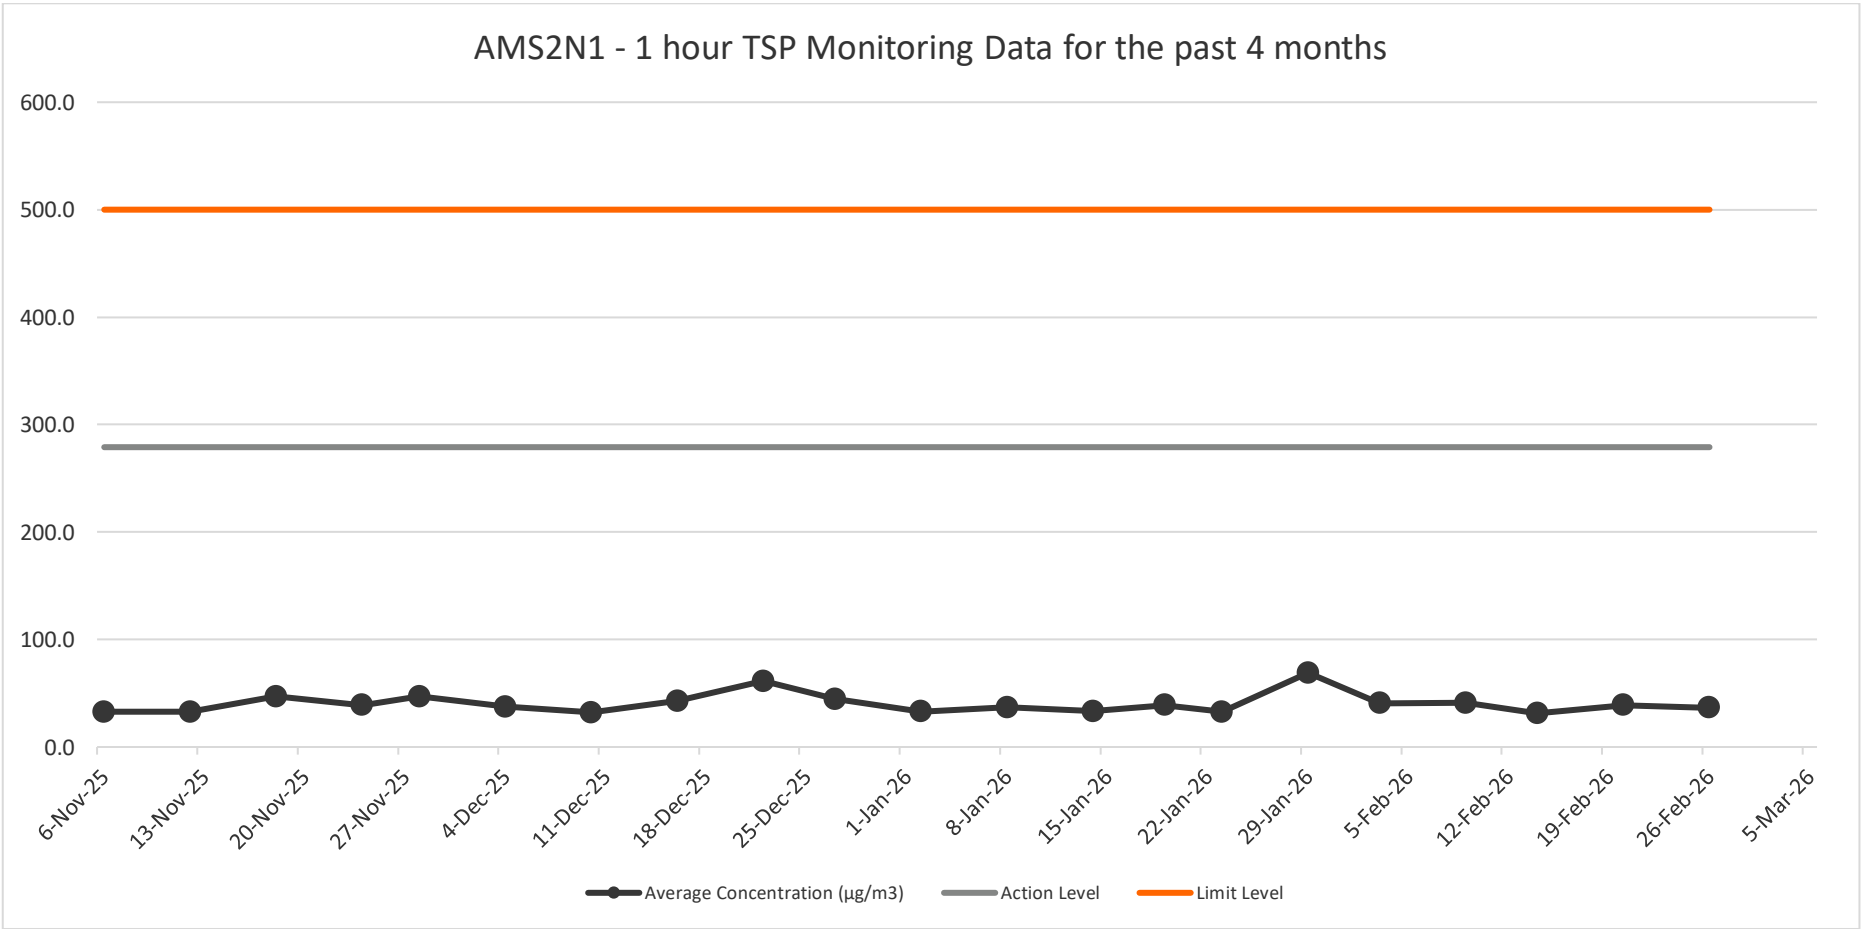

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	G-11
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

AMS2N1- 24 – hour TSP Monitoring

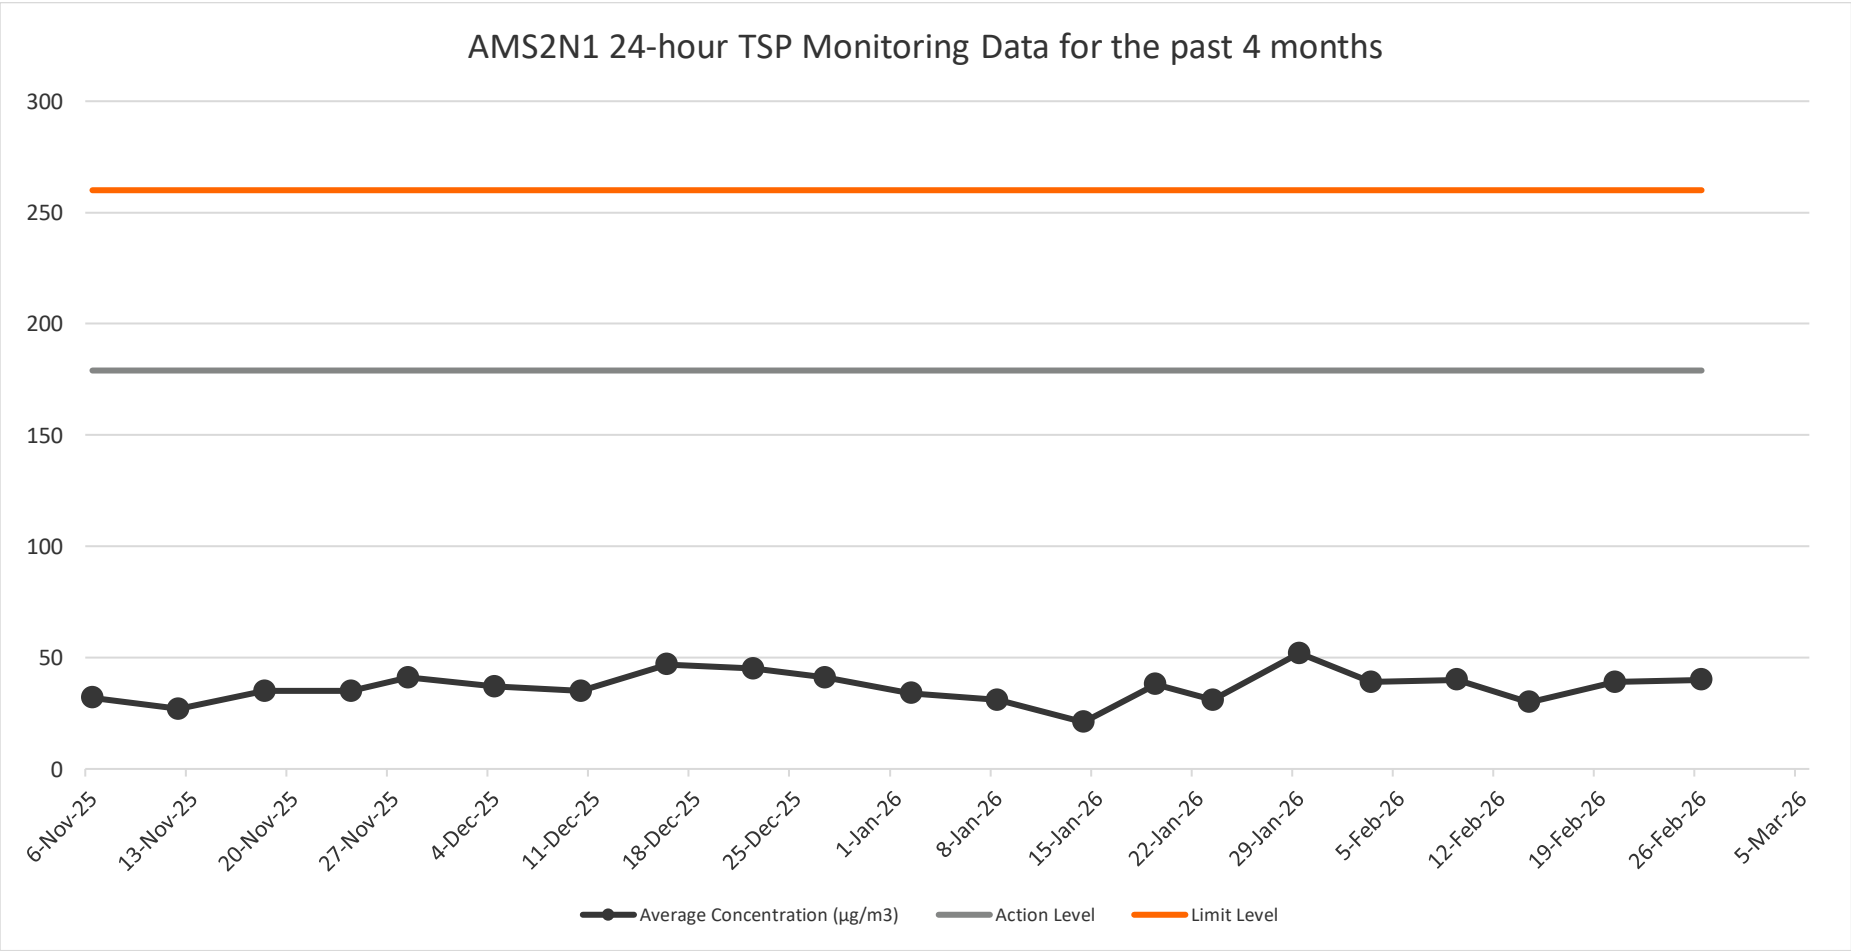

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	G-12
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

AMS3N – 1- hour and 24-hour TSP Monitoring

Date	Weather	1-hour TSP Monitoring	24-hour TSP monitoring
		Average Concentration (µg/m3)	Average Concentration (µg/m3)
4- Dec -25	Cloudy	31.7	32.0
10- Dec -25	Cloudy	31.7	33.0
16- Dec -25	Fine	37.3	42.0
22- Dec -25	Fine	53.7	44.0
27- Dec -25	Fine	40.3	41.0

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	G-13
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26


Date	Weather	1-hour TSP Monitoring	24-hour TSP monitoring
		Average Concentration (µg/m3)	Average Concentration (µg/m3)
2- Jan -26	Sunny	33.3	34.0
8- Jan -26	Fine	33.3	35.0
14- Jan -26	Fine	31.3	44.0
19- Jan -26	Sunny	43.3	40.0
23- Jan -26	Cloudy	32.0	30.0
28- Jan -26	Fine	67.3	51.0

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	G-14
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

Date	Weather	1-hour TSP Monitoring	24-hour TSP Monitoring
		Average Concentration (µg/m3)	Average Concentration (µg/m3)
3- Feb -26	Sunny	44.0	44.0
9- Feb -26	Sunny	47.7	46.0
14- Feb -26	Fine	25.7	27.0
20- Feb -26	Sunny	43.3	43.0
26- Feb -26	Cloudy	44.3	40.0
	Average:	40.0	39.1
	Action Level:	303	158
	Limit Level:	500	260


	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	G-15
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

AMS3N- 1 – hour TSP Monitoring

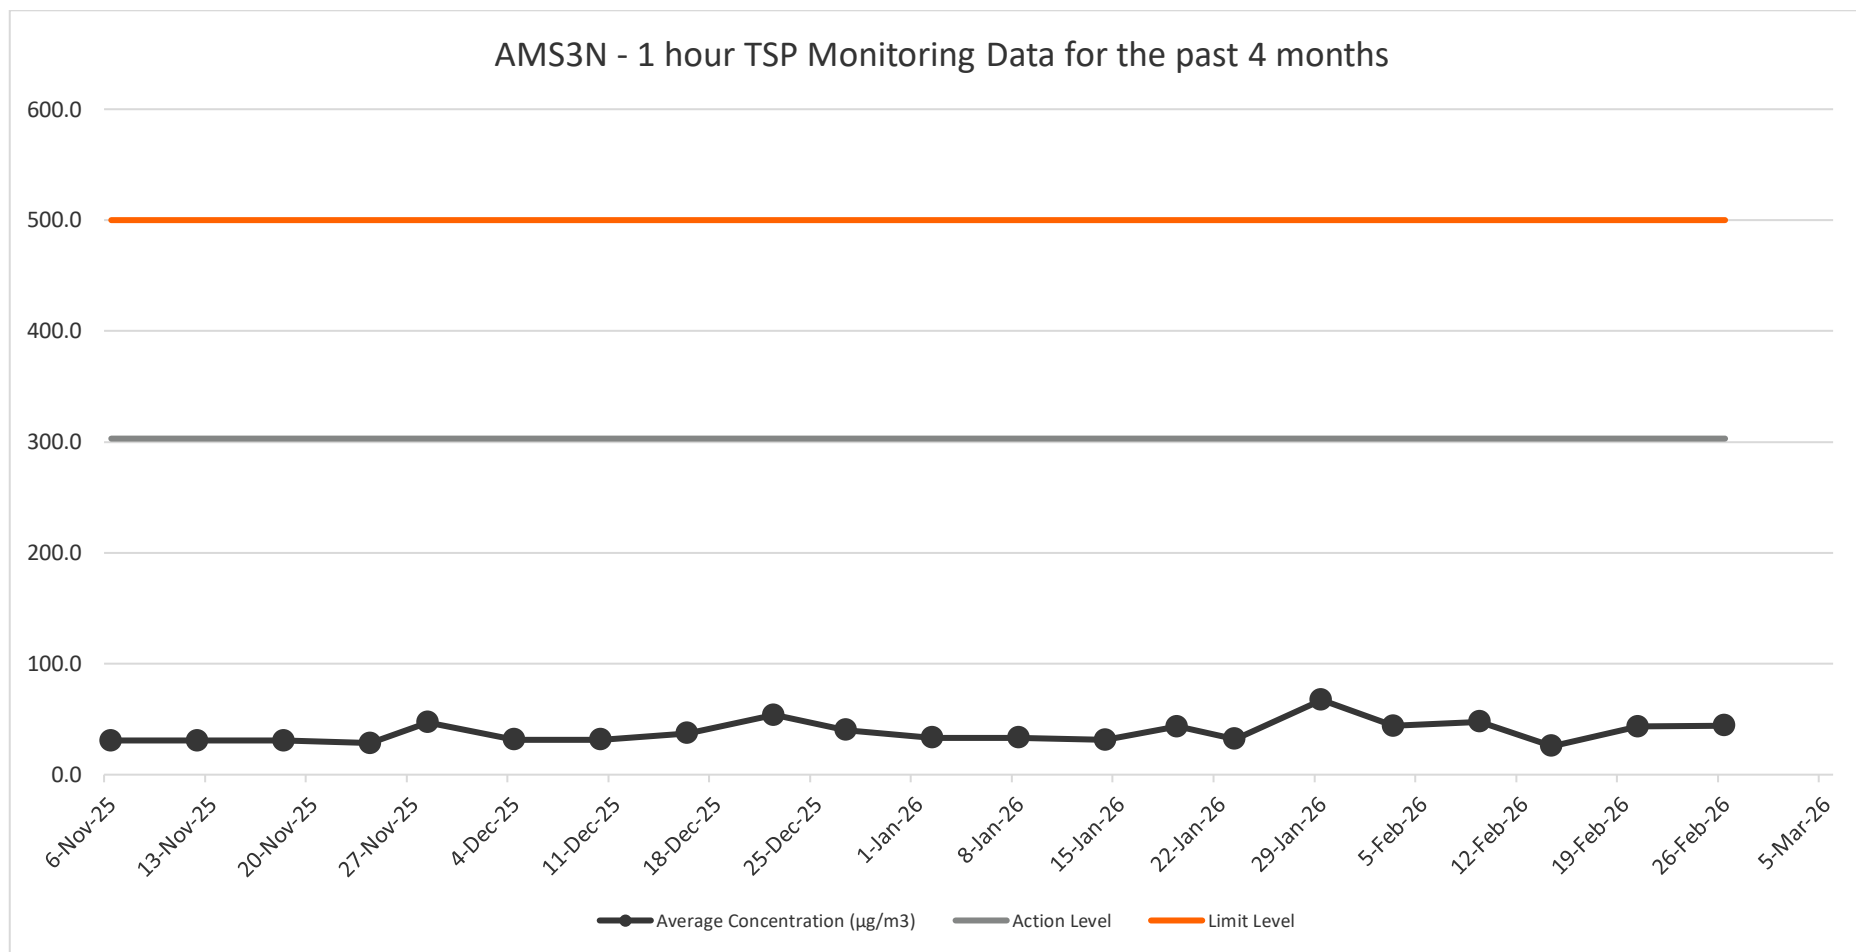

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	G-17
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

AMS3N – 24-hour TSP Monitoring

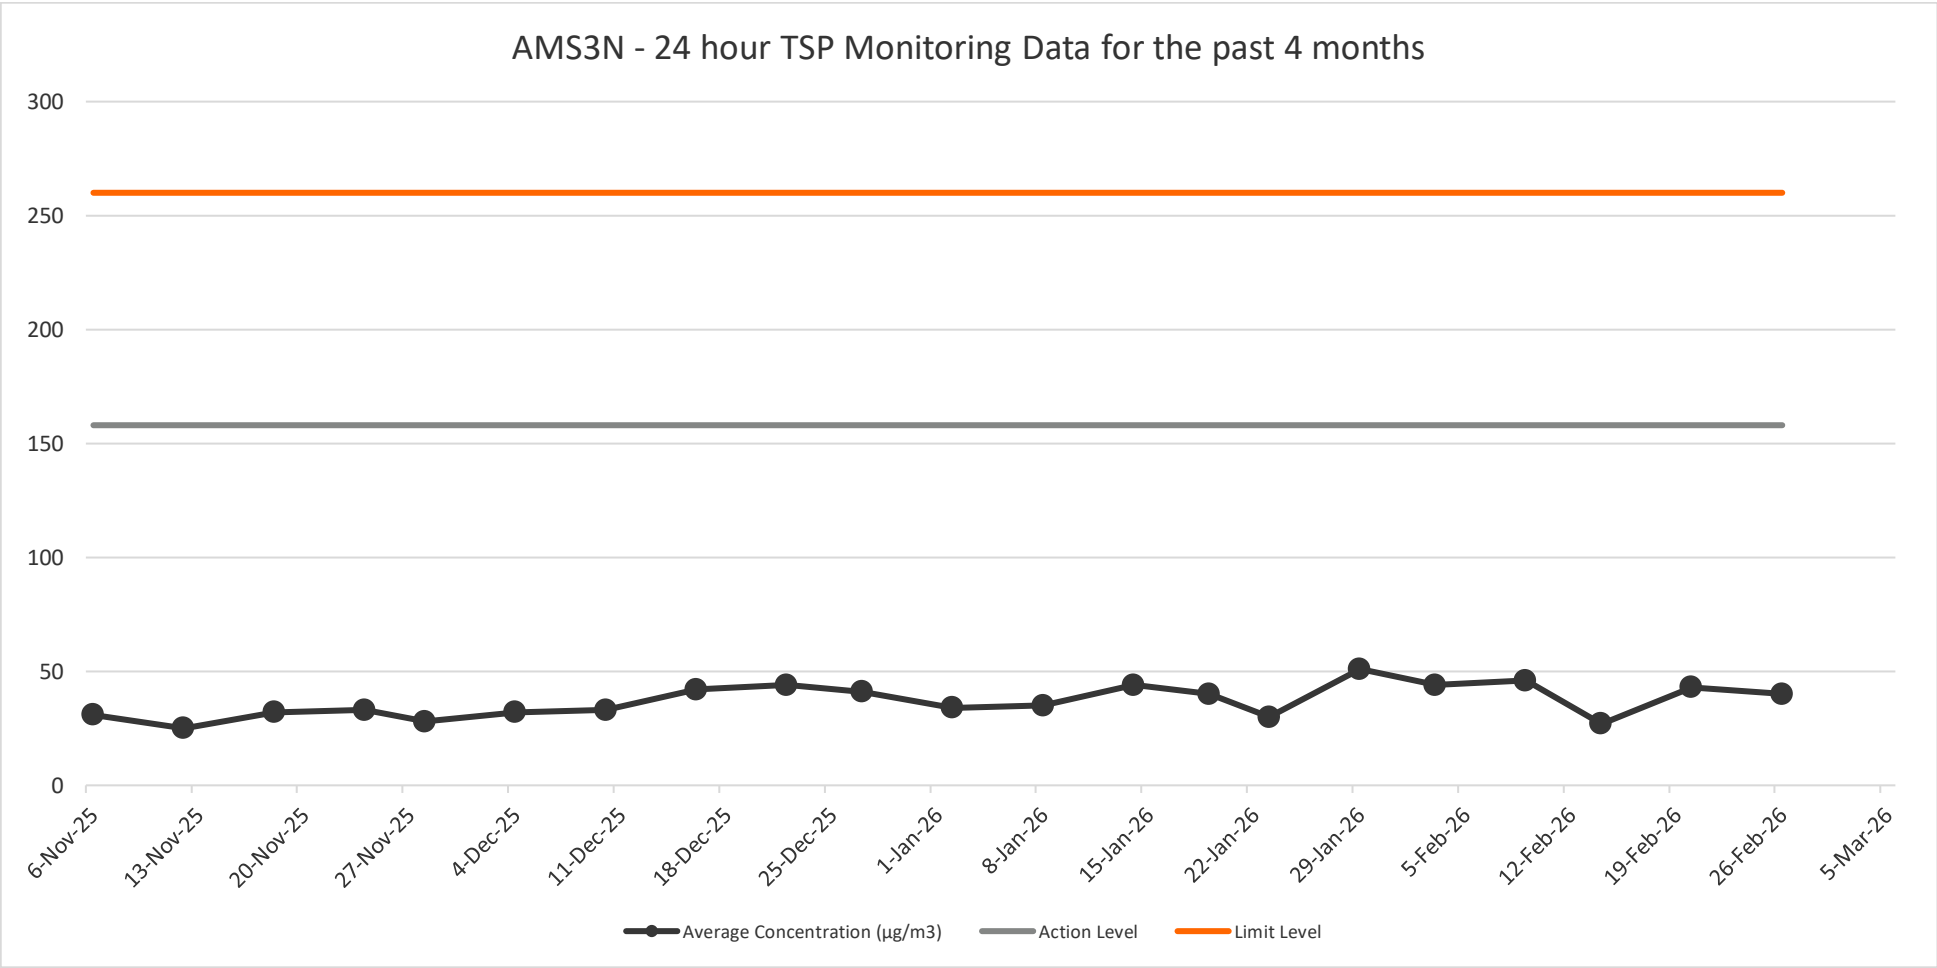

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	G-17
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

AMS4N — 1- hour and 24-hour TSP Monitoring

Date	Weather	1-hour TSP Monitoring	24-hour TSP monitoring
		Average Concentration (µg/m3)	Average Concentration (µg/m3)
4- Dec -25	Cloudy	30.3	32.0
10- Dec -25	Cloudy	23.3	26.0
16- Dec -25	Fine	31.7	35.0
22- Dec -25	Fine	56.0	42.0
27- Dec -25	Fine	29.7	30.0

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	G-18
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26


Date	Weather	1-hour TSP Monitoring	24-hour TSP monitoring
		Average Concentration (µg/m3)	Average Concentration (µg/m3)
2- Jan -26	Sunny	21.3	23.0
8- Jan -26	Fine	21.7	23.0
14- Jan -26	Fine	26.7	19.0
19- Jan -26	Sunny	29.0	27.0
23- Jan -26	Cloudy	23.3	21.0
28- Jan -26	Fine	65.7	51.0

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	G-19
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

Date	Weather	1-hour TSP Monitoring	24-hour TSP Monitoring
		Average Concentration (µg/m3)	Average Concentration (µg/m3)
3- Feb -26	Sunny	28.7	30.0
9- Feb -26	Sunny	26.3	24.0
14- Feb -26	Fine	29.3	21.0
20- Feb -26	Sunny	29.0	28.0
26- Feb -26	Cloudy	30.7	27.0
	Average:	31.4	28.7
	Action Level:	278	144
	Limit Level:	500	260


	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	G-20
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

AMS4N- 1 – hour TSP Monitoring

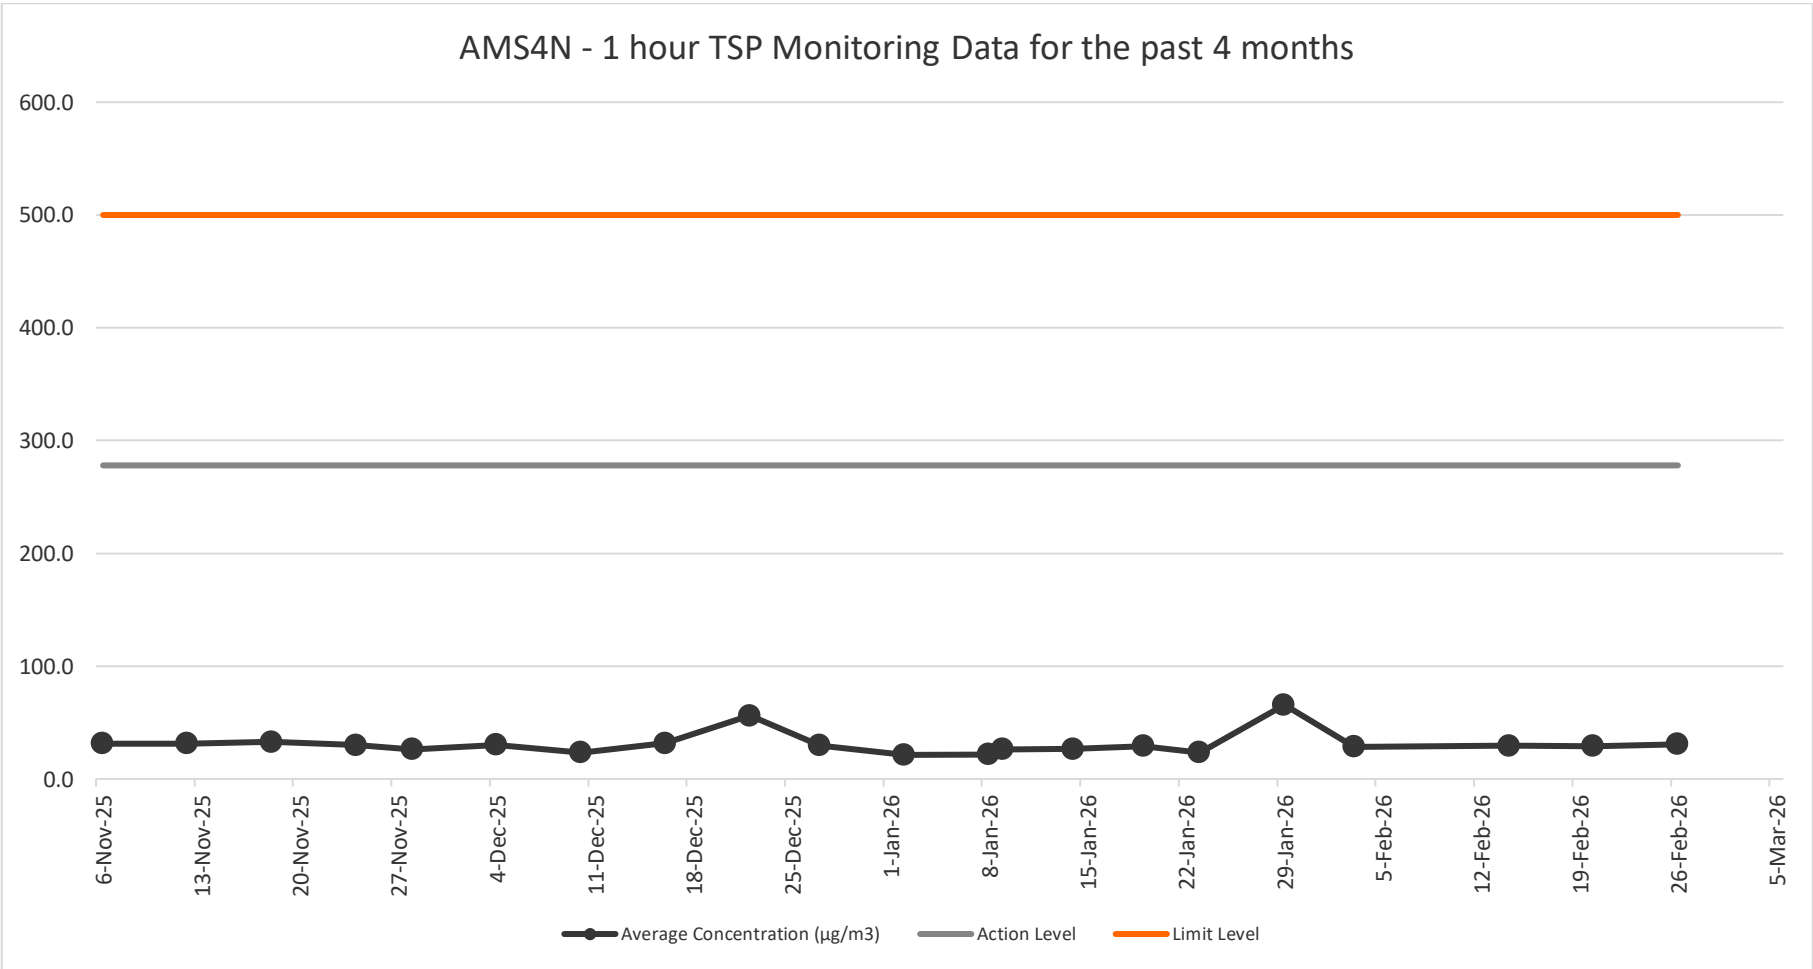

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	G-21
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

AMS4N- 24 – hour TSP Monitoring

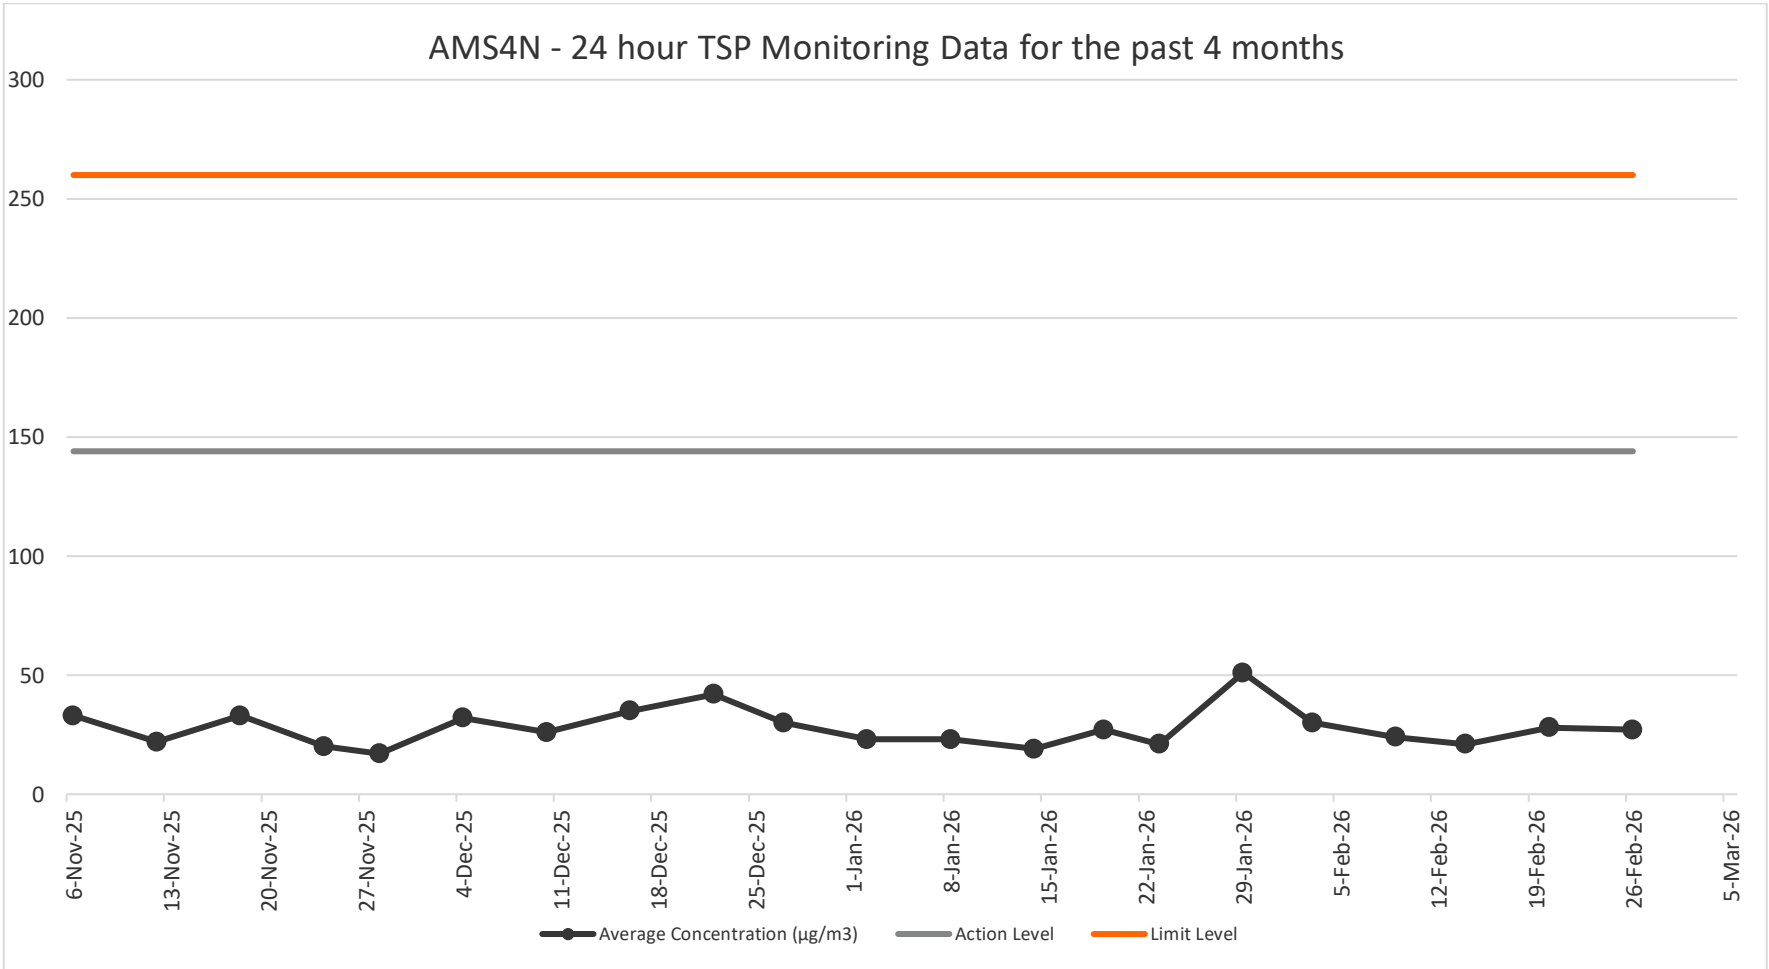


	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	G-22
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

NMS1N – Leq30 Noise monitoring

Start Date & Time	Weather	Leq dB(A)	L90 dB(A)	L10 dB(A)	Limit Level:
4- Dec -25	Cloudy	59.2	52.9	65.9	75
10- Dec -25	Cloudy	52.6	50.0	57.8	75
16- Dec -25	Fine	49.1	39.8	51.4	75
27- Dec -25	Fine	51.3	40.1	54.0	75
2- Jan -26	Sunny	66.9	64.3	69.4	75
8- Jan -26	Fine	64.1	60.3	65.5	75
14- Jan -26	Fine	63.0	59.6	64.8	75
19- Jan -26	Sunny	62.7	62.5	69.3	75
28- Jan -26	Fine	67.5	62.4	67.6	75
3- Feb -26	Sunny	50.6	46.6	53.6	75
9- Feb -26	Sunny	52.5	47.4	55.6	75
20- Feb -26	Sunny	66.9	64.3	68.4	75
26- Feb -26	Cloudy	62.4	61.1	64.2	75
Action Level:	When one valid documented complaint is received				
Limit Level:	75.0 dB(A)				

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		Page	G-23
			Ref#	-
	Quarterly EM&A Report		Rev.	01
			Date	Mar 26

NMS1N – Leq30 Noise monitoring

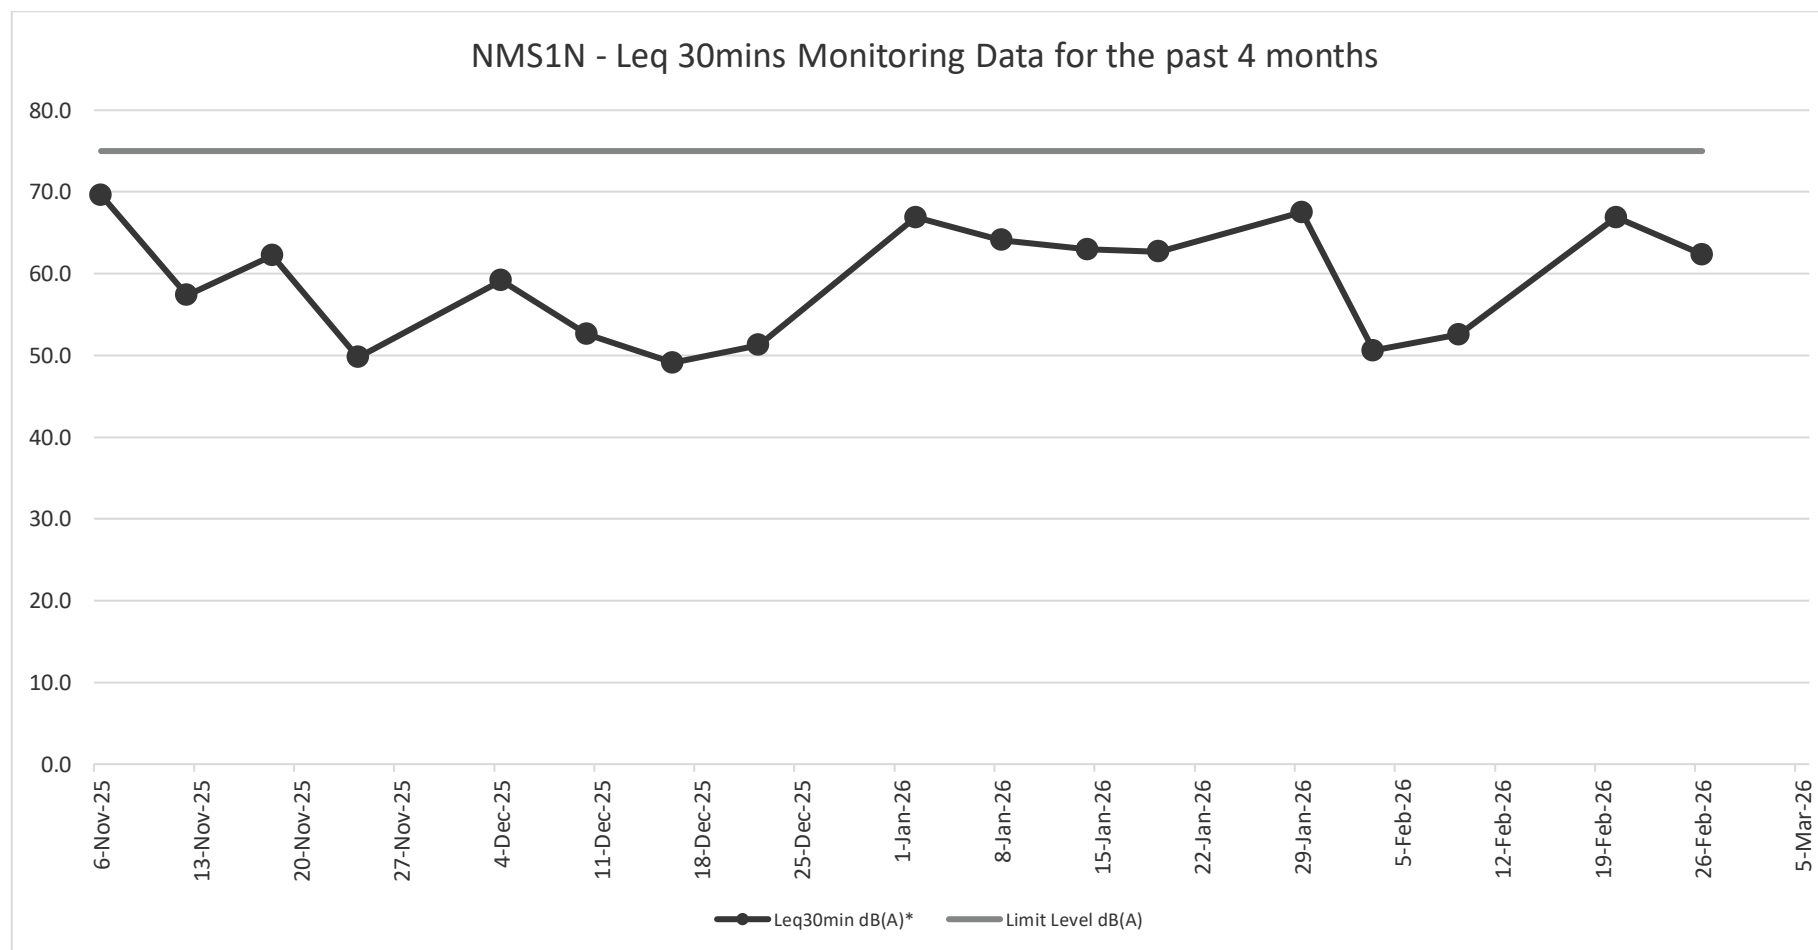


	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	G-24
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

NMS2N1 – Leq30 Noise monitoring

Start Date & Time	Weather	Leq dB(A)	L90 dB(A)	L10 dB(A)	Limit Level:
4- Dec -25	Cloudy	56.3	54.4	62.7	75
10- Dec -25	Cloudy	55.6	52.7	59.3	75
16- Dec -25	Fine	55.5	44.9	59.6	75
27- Dec -25	Fine	53.4	44.1	57.2	75
2- Jan -26	Sunny	55.8	52.4	56.9	75
8- Jan -26	Fine	60.4	57.0	61.9	75
14- Jan -26	Fine	58.4	55.6	60.1	75
19- Jan -26	Sunny	56.0	52.4	57.2	75
28- Jan -26	Fine	58.8	53.6	61.7	75
3- Feb -26	Sunny	63.6	51.7	66.3	75
9- Feb -26	Sunny	61.4	55.5	64.3	75
20- Feb -26	Sunny	55.9	52.6	57.3	75
26- Feb -26	Cloudy	53.8	50.5	56.1	75
Action Level:	When one valid documented complaint is received				
Limit Level:	75.0 dB(A)				

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	G-25
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

NMS2N1 – Leq30 Noise monitoring

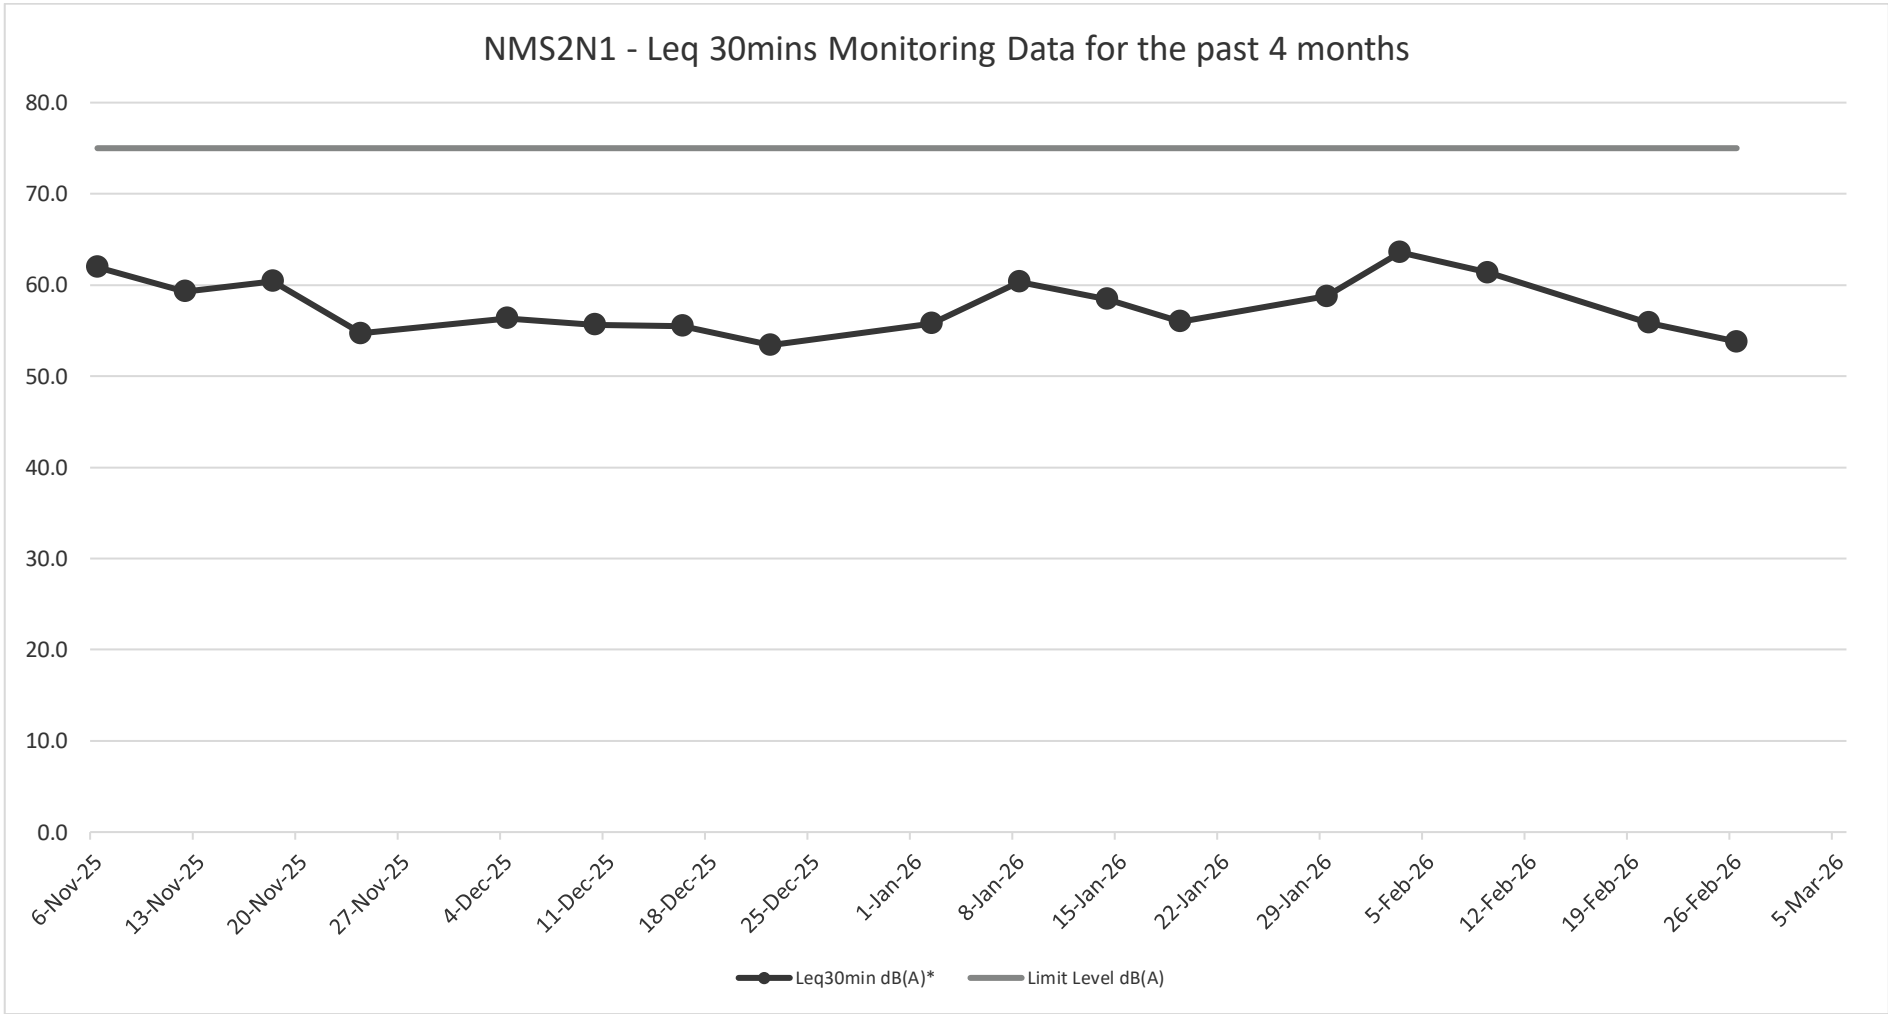


	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	G-26
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

NMS3N – Leq30 Noise monitoring

Start Date & Time	Weather	Leq dB(A)	L90 dB(A)	L10 dB(A)	Limit Level:
4- Dec -25	Cloudy	58.9	57.2	62.2	75
10- Dec -25	Cloudy	56.6	54.0	59.3	75
16- Dec -25	Fine	54.2	47.8	58.5	75
27- Dec -25	Fine	55.8	47.3	60.2	75
2- Jan -26	Sunny	54.2	51.1	56.1	75
8- Jan -26	Fine	58.7	55.5	60.0	75
14- Jan -26	Fine	55.6	51.8	56.9	75
19- Jan -26	Sunny	53.6	51.0	55.7	75
28- Jan -26	Fine	56.4	51.3	58.8	75
3- Feb -26	Sunny	55.5	52.5	57.4	75
9- Feb -26	Sunny	67.7	49.8	71.4	75
20- Feb -26	Sunny	53.7	51.9	57.6	75
26- Feb -26	Cloudy	62.6	59.0	65.8	75
Action Level:	When one valid documented complaint is received				
Limit Level:	75.0 dB(A)				

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	G-27
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

NMS3N – Leq30 Noise monitoring

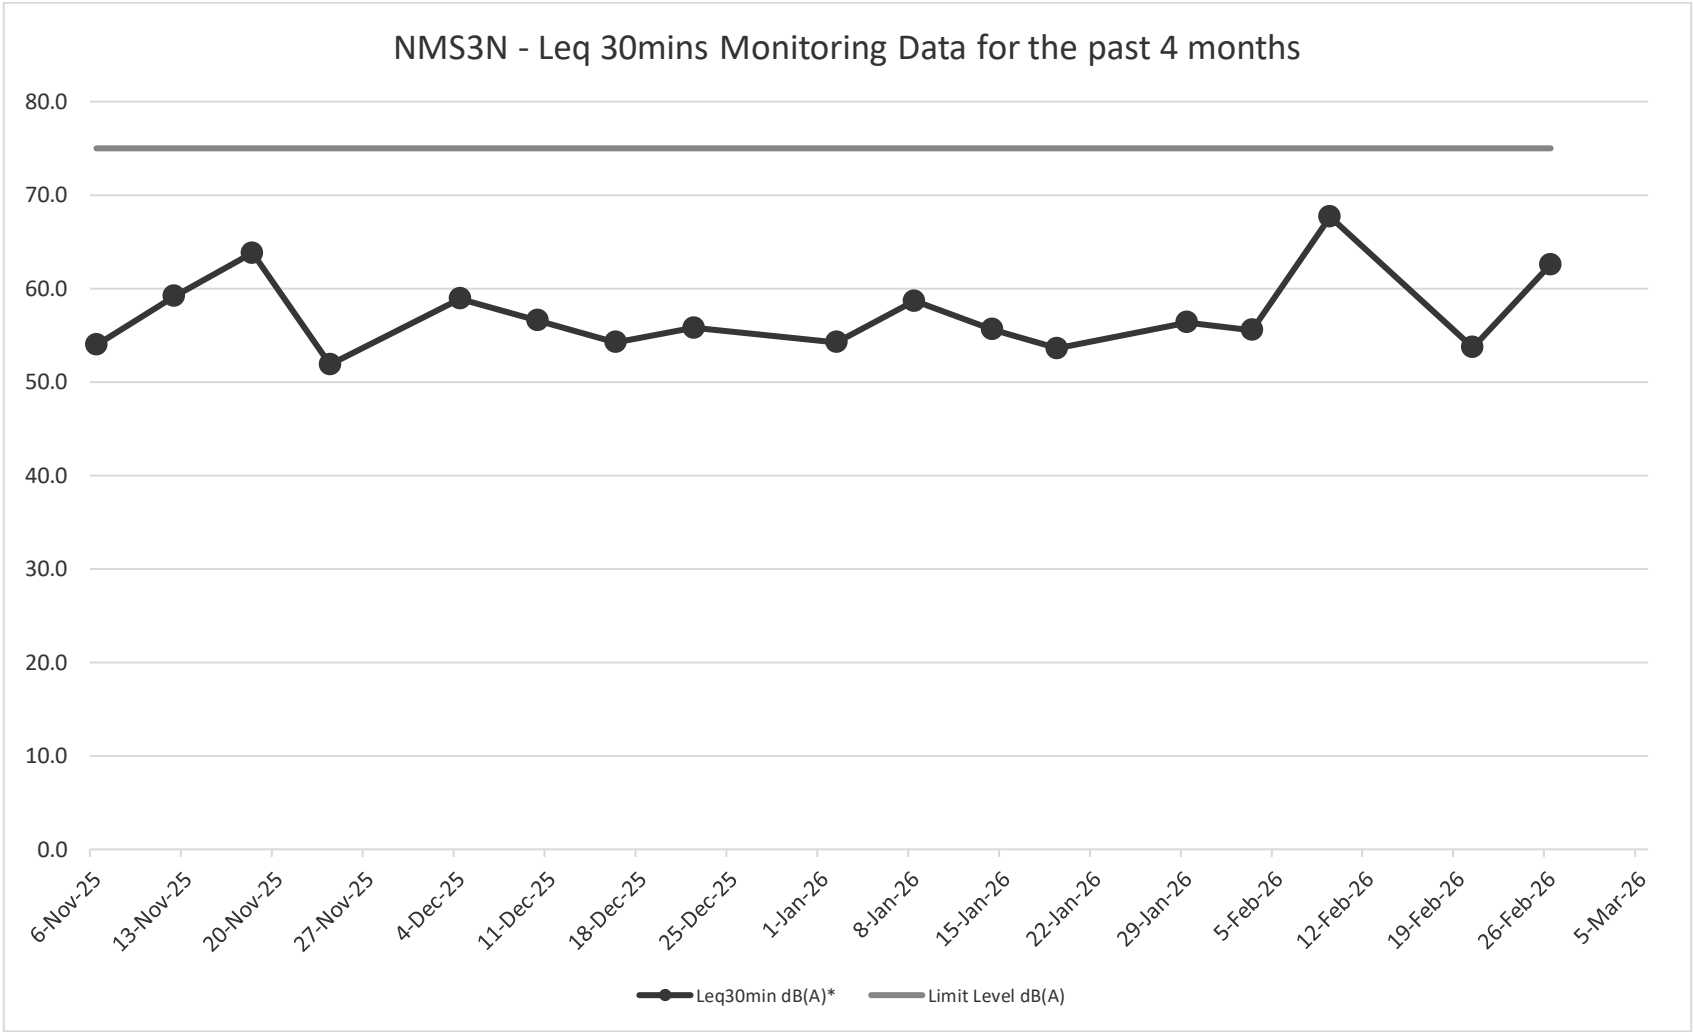


	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	G-28
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

NMS4N – Leq30 Noise monitoring

Start Date & Time	Weather	Leq dB(A)	L90 dB(A)	L10 dB(A)	Limit Level:
4- Dec -25	Cloudy	54.9	53.7	59.4	75
10- Dec -25	Cloudy	57.2	54.9	60.2	75
16- Dec -25	Fine	52.2	40.2	56.2	75
27- Dec -25	Fine	53.3	39.8	56.5	75
2- Jan -26	Sunny	46.6	43.7	48.4	75
8- Jan -26	Fine	48.0	45.1	49.6	75
14- Jan -26	Fine	49.3	45.6	50.7	75
19- Jan -26	Sunny	46.5	43.7	49.6	75
28- Jan -26	Fine	53.8	51.5	55.4	75
3- Feb -26	Sunny	63.5	45.6	67.4	75
9- Feb -26	Sunny	67.6	49.6	72.1	75
20- Feb -26	Sunny	47.1	43.3	57.0	75
26- Feb -26	Cloudy	56.3	53.4	58.2	75
Action Level:	When one valid documented complaint is received				
Limit Level:	75.0 dB(A)				

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	G-29
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

NMS4N – Leq30 Noise monitoring

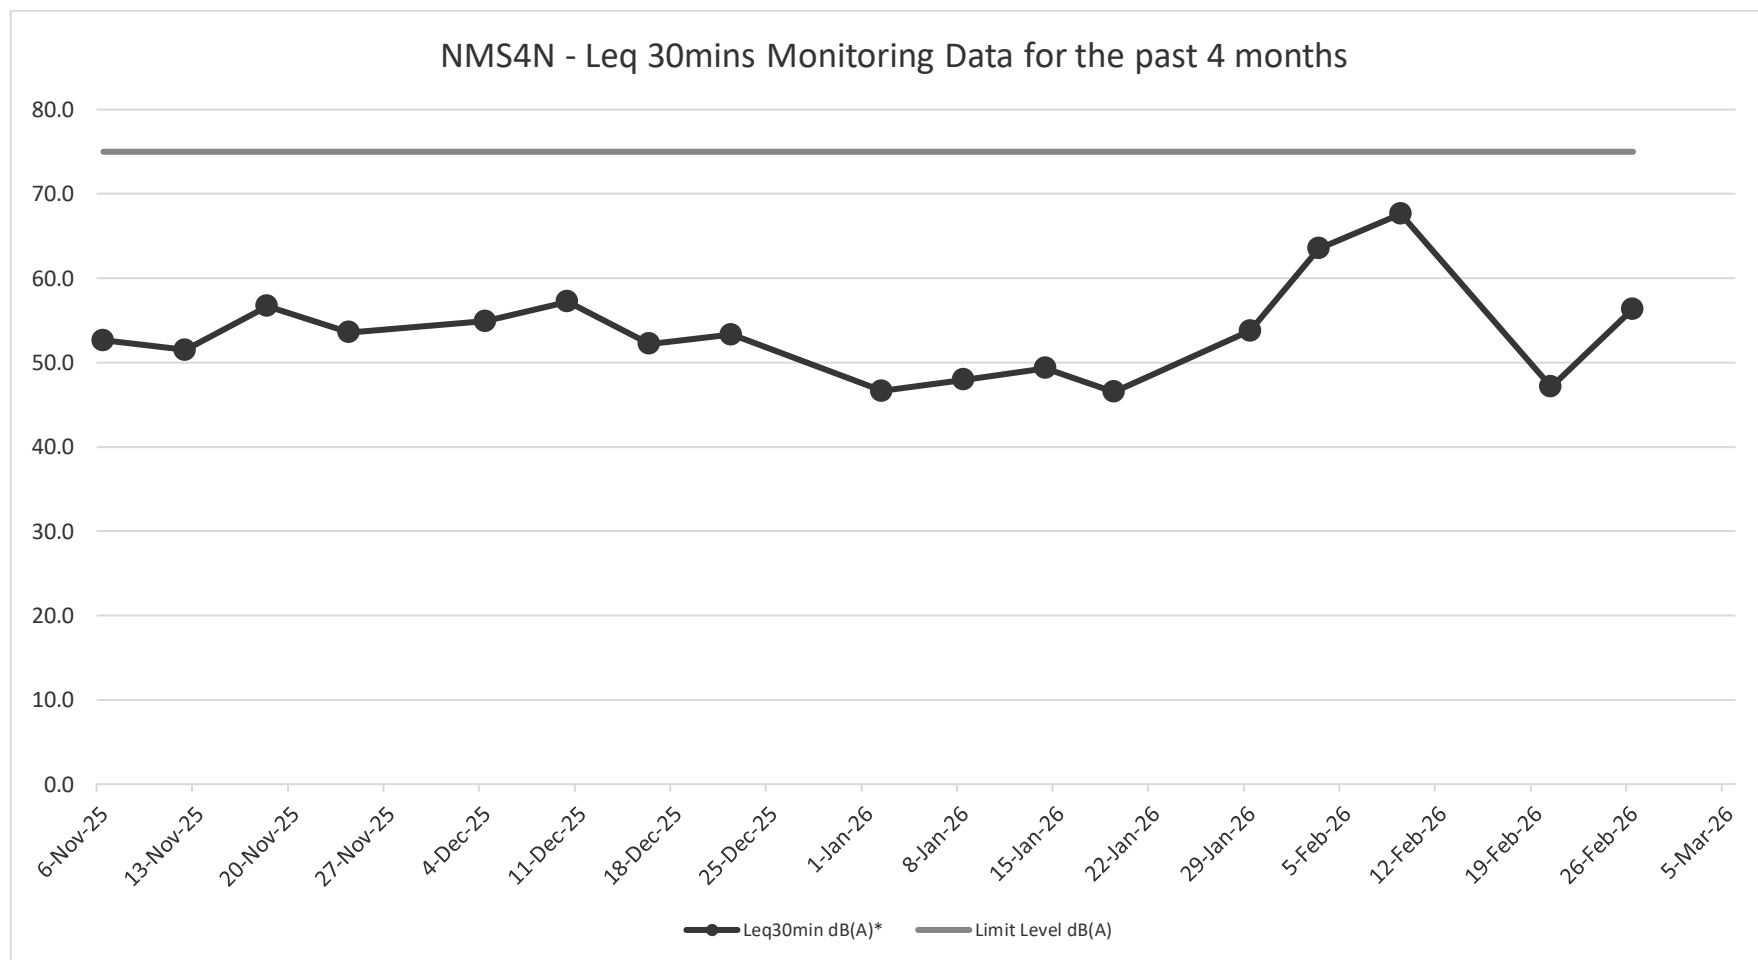

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		Page	H-1
			Ref#	-
	Quarterly EM&A Report		Rev.	01
			Date	Mar 26

APPENDIX H - SUMMARY OF WASTE FLOW TABLE

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	H-2
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

Monthly Summary Waste Flow Table for 2025 Year

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposal as Public Fill	Imported Fill	Metals	Paper / Cardboard Packaging	Plastics (see note 3)	Chemical Waste	Other, e.g. general refuse
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	[in '000kg]	[in '000kg]	[in '000kg]	[in '000kg]	[in Tonne]
Jan	0.003	0.000	0.000	0.000	0.003	0.000	0.000	0.000	0.000	0.000	0.000
Feb	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Mar	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Apr	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
May	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Jun	0.085	0.000	0.000	0.000	0.085	0.000	0.000	0.000	0.000	0.000	3.67
Sub-Total	0.088	0.000	0.000	0.000	0.088	0.000	0.000	0.000	0.000	0.000	3.67
Jul	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	8.34
Aug	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	11.76
Sep	0.003	0.000	0.000	0.000	0.003	0.000	0.000	0.000	0.000	0.000	10.37
Oct	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	4.13
Feb	0.050	0.000	0.000	0.000	0.050	0.000	0.000	0.000	0.000	0.000	0.000
Dec	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Total	0.141	0.000	0.000	0.000	0.141	0.000	0.000	0.000	0.000	0.000	38.27

- Note:**
- (1) The performance targets are given in the Environmental Management Plan.
 - (2) The waste flow table shall also include C&D materials to be imported for use at the Site.
 - (3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material.

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	H-2
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

Monthly Summary Waste Flow Table for 2026 Year

Month	Actual Quantities of Inert C&D Materials Generated Monthly						Actual Quantities of C&D Wastes Generated Monthly				
	Total Quantity Generated	Hard Rock and Large Broken Concrete	Reused in the Contract	Reused in other Projects	Disposal as Public Fill	Imported Fill	Metals	Paper / Cardboard Packaging	Plastics (see note 3)	Chemical Waste	Other, e.g. general refuse
	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	(in '000m ³)	[in '000kg]	[in '000kg]	[in '000kg]	[in '000kg]	[in Tonne]
Jan	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Feb	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Mar											
Apr											
May											
Jun											
Sub-Total	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000
Jul											
Aug											
Sep											
Oct											
Feb											
Dec											
Total	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000	0.000

- Note:**
- (1) The performance targets are given in the Environmental Management Plan.
 - (2) The waste flow table shall also include C&D materials to be imported for use at the Site.
 - (3) Plastics refer to plastic bottles/containers, plastic sheets/foam from packaging material.

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O		Page	I-1
			Ref#	-
	Quarterly EM&A Report		Rev.	01
			Date	Mar 26

APPENDIX I - CUMULATIVE STATISTICS ON COMPLAINTS, NOTIFICATIONS OF SUMMONS

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	J-1
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

Environmental Complaints Log

Complaint Log No.	Date of Complaint	Received From	Received By	Nature of Environmental Complaint	Relevant to the Construction Work of Project Site? (Y/N)	Investigation/ Mitigation Action	Status
001	28 December 2021	EPD	ET	Waste Management	N	The investigation report was submitted on 7 April 2022	Closed
002	23 September 2024	EPD	ET	Waste Management	N	The investigation report was submitted on 27 September 2024	Closed
003	26 February 2025	EPD	ET	Wastewater Management / Air & Noise	N	The investigation report was submitted on 5 March 2025	Closed

Remarks: * No Notifications of Summons or Successful Prosecutions were received during the reporting period.

	EP-516/2016 - Port Shelter Sewerage, Stage3 - Sewerage Works at Po Toi O	Page	J-2
		Ref#	-
	Quarterly EM&A Report	Rev.	01
		Date	Mar 26

Cumulative Statistics on Complaints, Notifications of Summons and Successful Prosecutions and Public Engagement Activities

Reporting Period	Complaints	Notifications of Summons and Prosecutions	Public Engagement Activities
2025/12	0	0	0
2026/01	0	0	0
2026/02	0	0	0
Cumulative Project-to-Date	3	0	0
